



<u>PRI</u>	<u>PROJECT DESCRIPTION</u>	<u>LOCATION</u>	<u>DESIRED COMPLETION DATE</u>	<u>TROOP TRAINING EFFORT (PLTWKS)</u>	<u>BASE MAINT/ CONTRACTS</u>	<u>PRELIM COST EST</u>	<u>NOTES</u>
1-86	Mechanized Maneuver Course						
	a. <u>PHASE I</u>						
	(1 Jun 86 - 1 Jan 87)						
1.	Mobility/Counter Mobility Course*	IC Area	20% by 1 Jun 86	5 weeks/2d CEB	Timber Harvest MCB	\$5,000	*To support Coun Obstacle Vehicle (COV) tests Jun-
2.	<u>Battle Run Area**</u>	IA, IE, IF, HA, HC areas	25-30% Timber Harvest		Timber Harvest MCB		**Work to start area & work sout southeast
3.	Soviet Strong Point	HD area		26 Weeks/2d CEB (Partial)			
4.	<u>Combat Trails</u>	872268 to 881281 879329 to 860311	1 Jan 87				
		<i>① SAILERS BAT ED.</i>					
		<i>② MARINES ED.</i>					
5.	Tank Crossing Pads	857289 881281	1 Jan 87				


*Nothing being done on Env. Assessment*

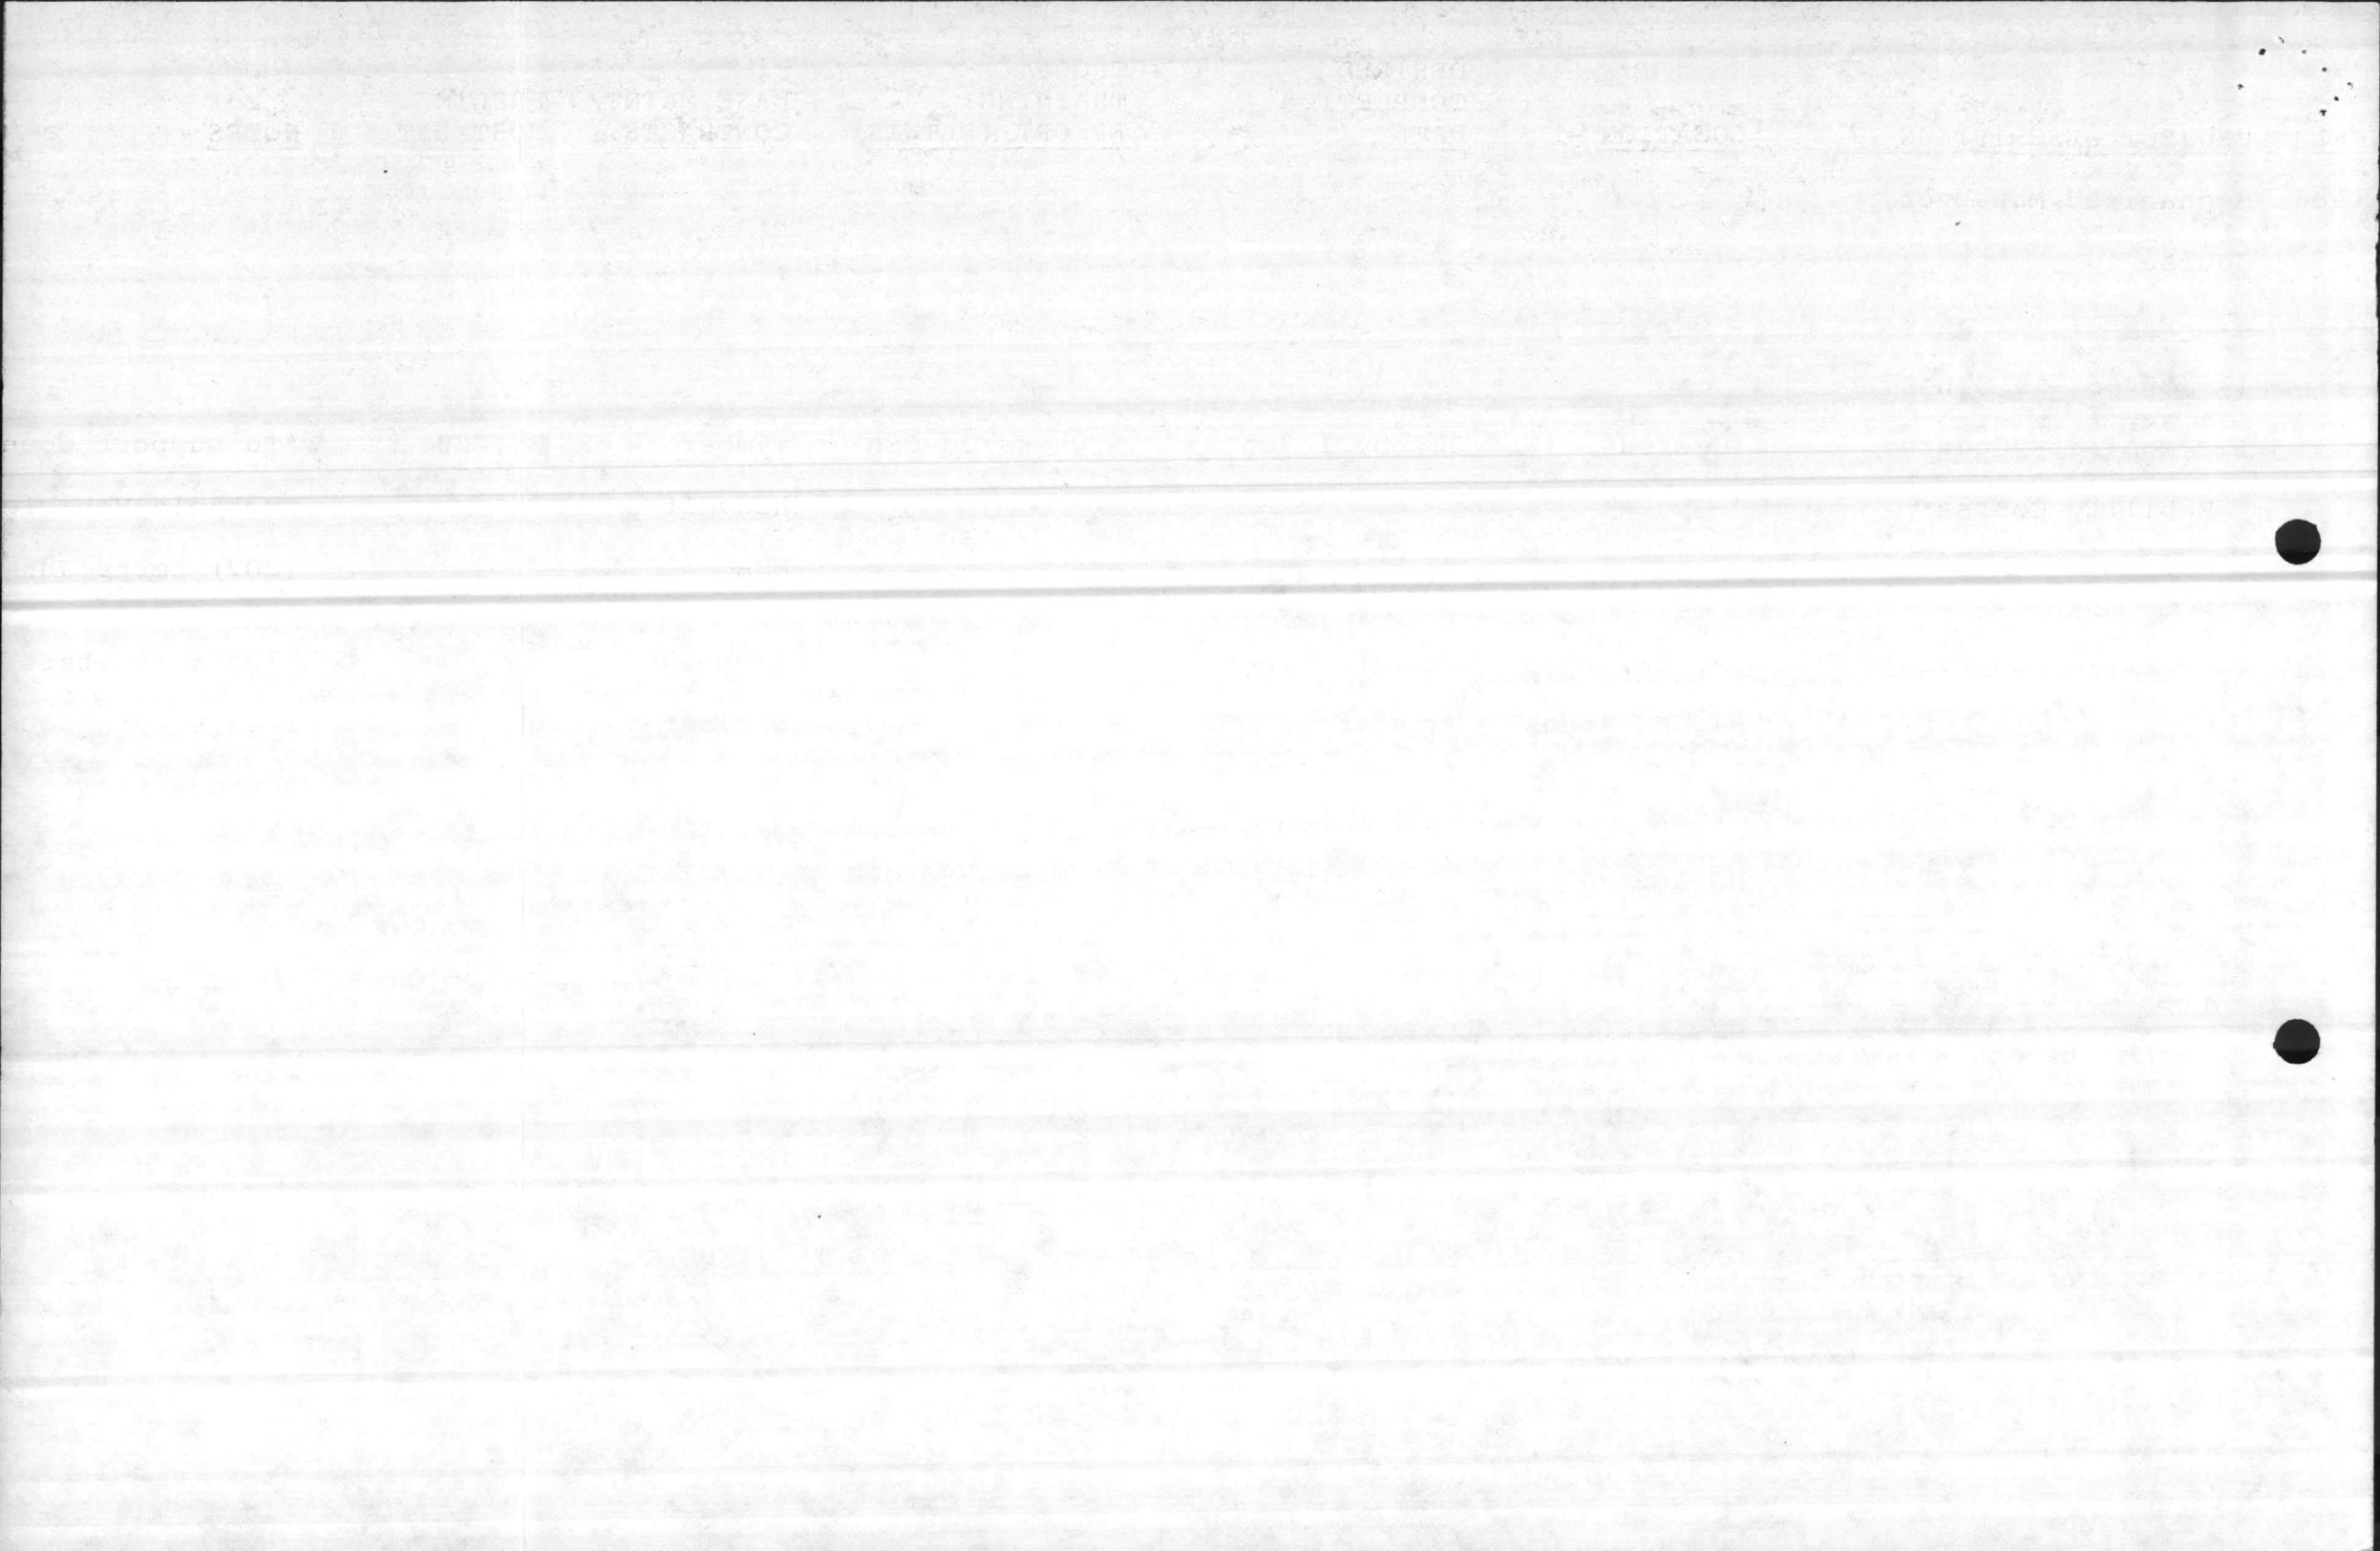


<u>PRI</u>	<u>PROJECT DESCRIPTION</u>	<u>LOCATION</u>	<u>DESIRED COMPLETION DATE</u>	<u>TROOP TRAINING EFFORT (PLTWKS)</u>	<u>BASE MAINT/ CONTRACTS</u>	<u>PRELIM COST EST</u>	<u>NOTES</u>
	6. Culvert	875273 878275	1 Jan 87				
	b. <u>PHASE II</u> (1 Jan 87 - 1 Jul 87)						
	1. Mobility/Counter Mobility Course	IC area	75% by 1 Jul 87				
	2. <u>Battle Run Area</u>	IA, IE, IF, HA, HC area	50-75% by 1 Jul 87		Timber Harvest		
	3. Soviet Strong Point	HD area	25% by 1 Jul 87				
	4. <u>Combat Trails</u>	863281 to 861288 <sup>③ traps</sup> 906297 to 902289 <sup>② GUNETS</sup>	1 Jul 87				
	5. Tank Crossing Pads	838305 845292 849312 902289					

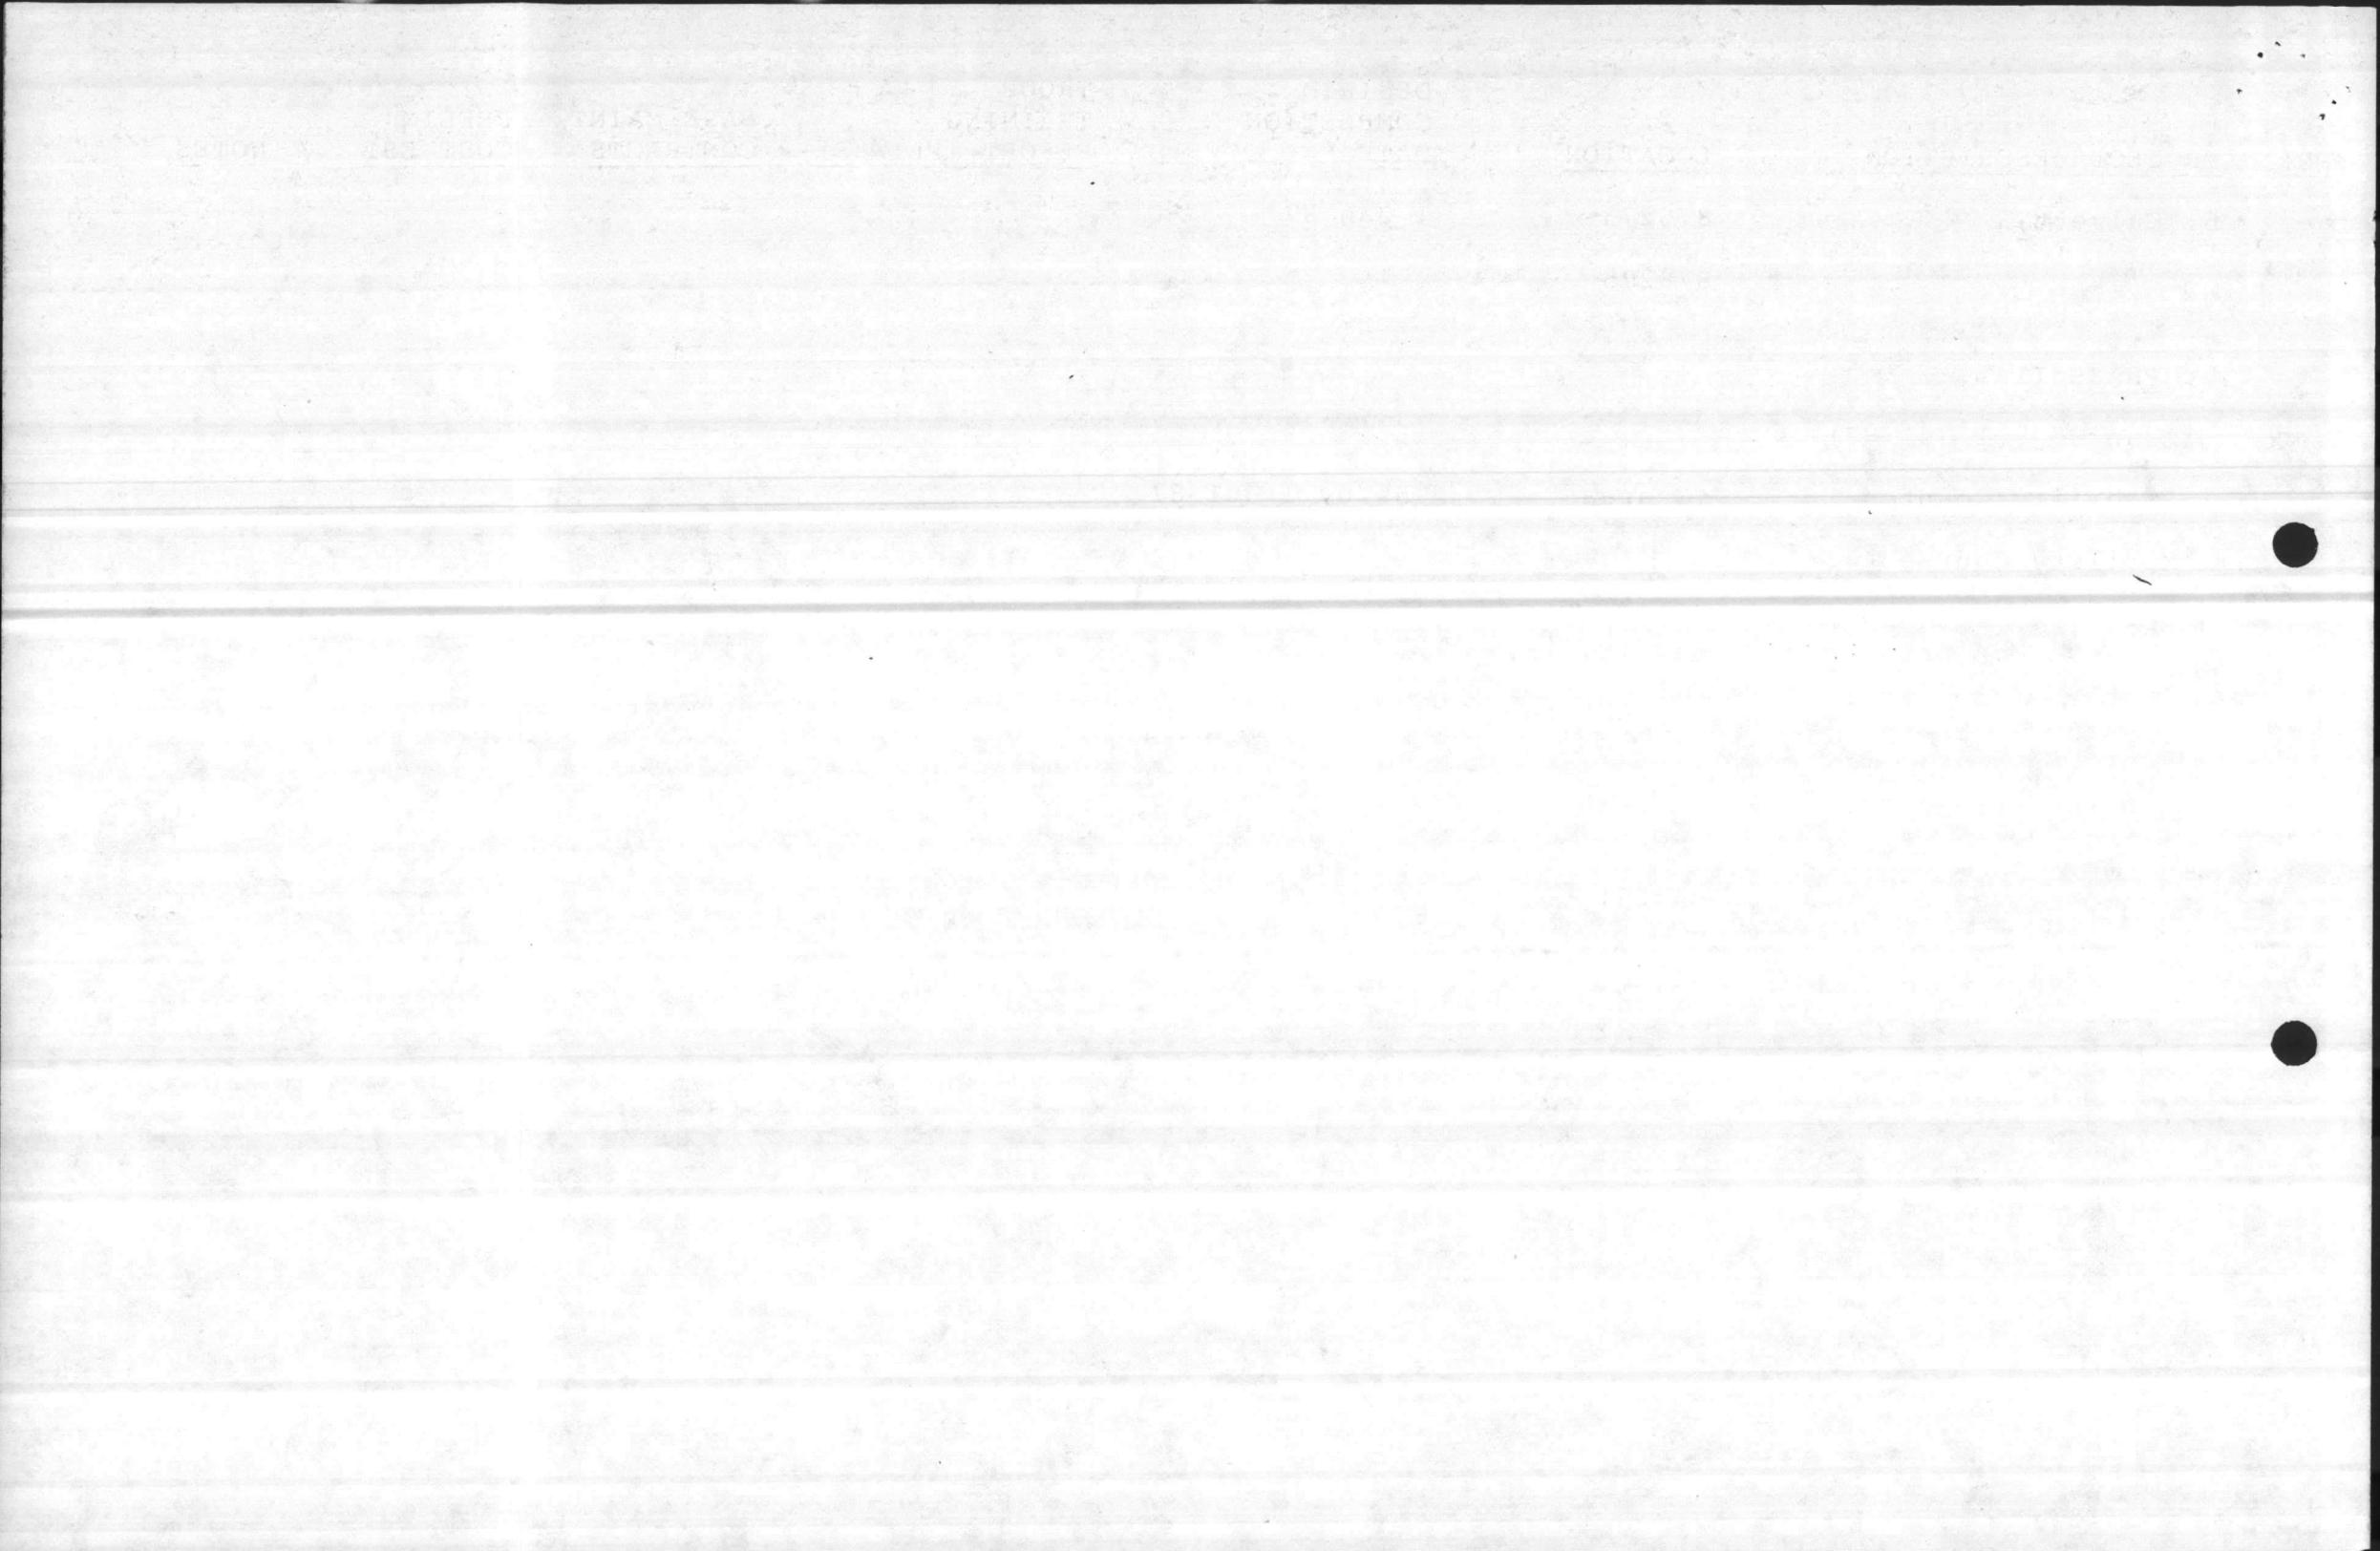


<u>PRI.</u>	<u>PROJECT DESCRIPTION</u>	<u>LOCATION</u>	<u>DESIRED COMPLETION DATE</u>	<u>TROOP TRAINING EFFORT (PLTWKS)</u>	<u>BASE MAINT/ CONTRACTS</u>	<u>PRELIM COST EST</u>	<u>NOTES</u>
	6. Bridging Sites	862284					
		857274					
	7. Splashpoint	824312	1 Jul 87				
	c. <u>PHASE III</u>						
	(1 Jul 87 - 1 Jan 88)						
	1. <u>Mobility/Counter</u>						
	Mobility Course						
	2. <u>Battle Run Area</u>		75-100% if Timber				
			<u>Harvest by 1 Jan 88</u>				
	3. Soviet Strong Point						
	4. <u>Combat Trails</u>	881281 to					
		869305					<i>5 Answer cc.</i>
		865318 to					
		866332					<i>5 Duce Co.</i>
	5. Tank Crossing Pads	865318	1 Jan 88				
	6. Bridge	866328					
	7. Splashpoints	828315	1 Jan 88				

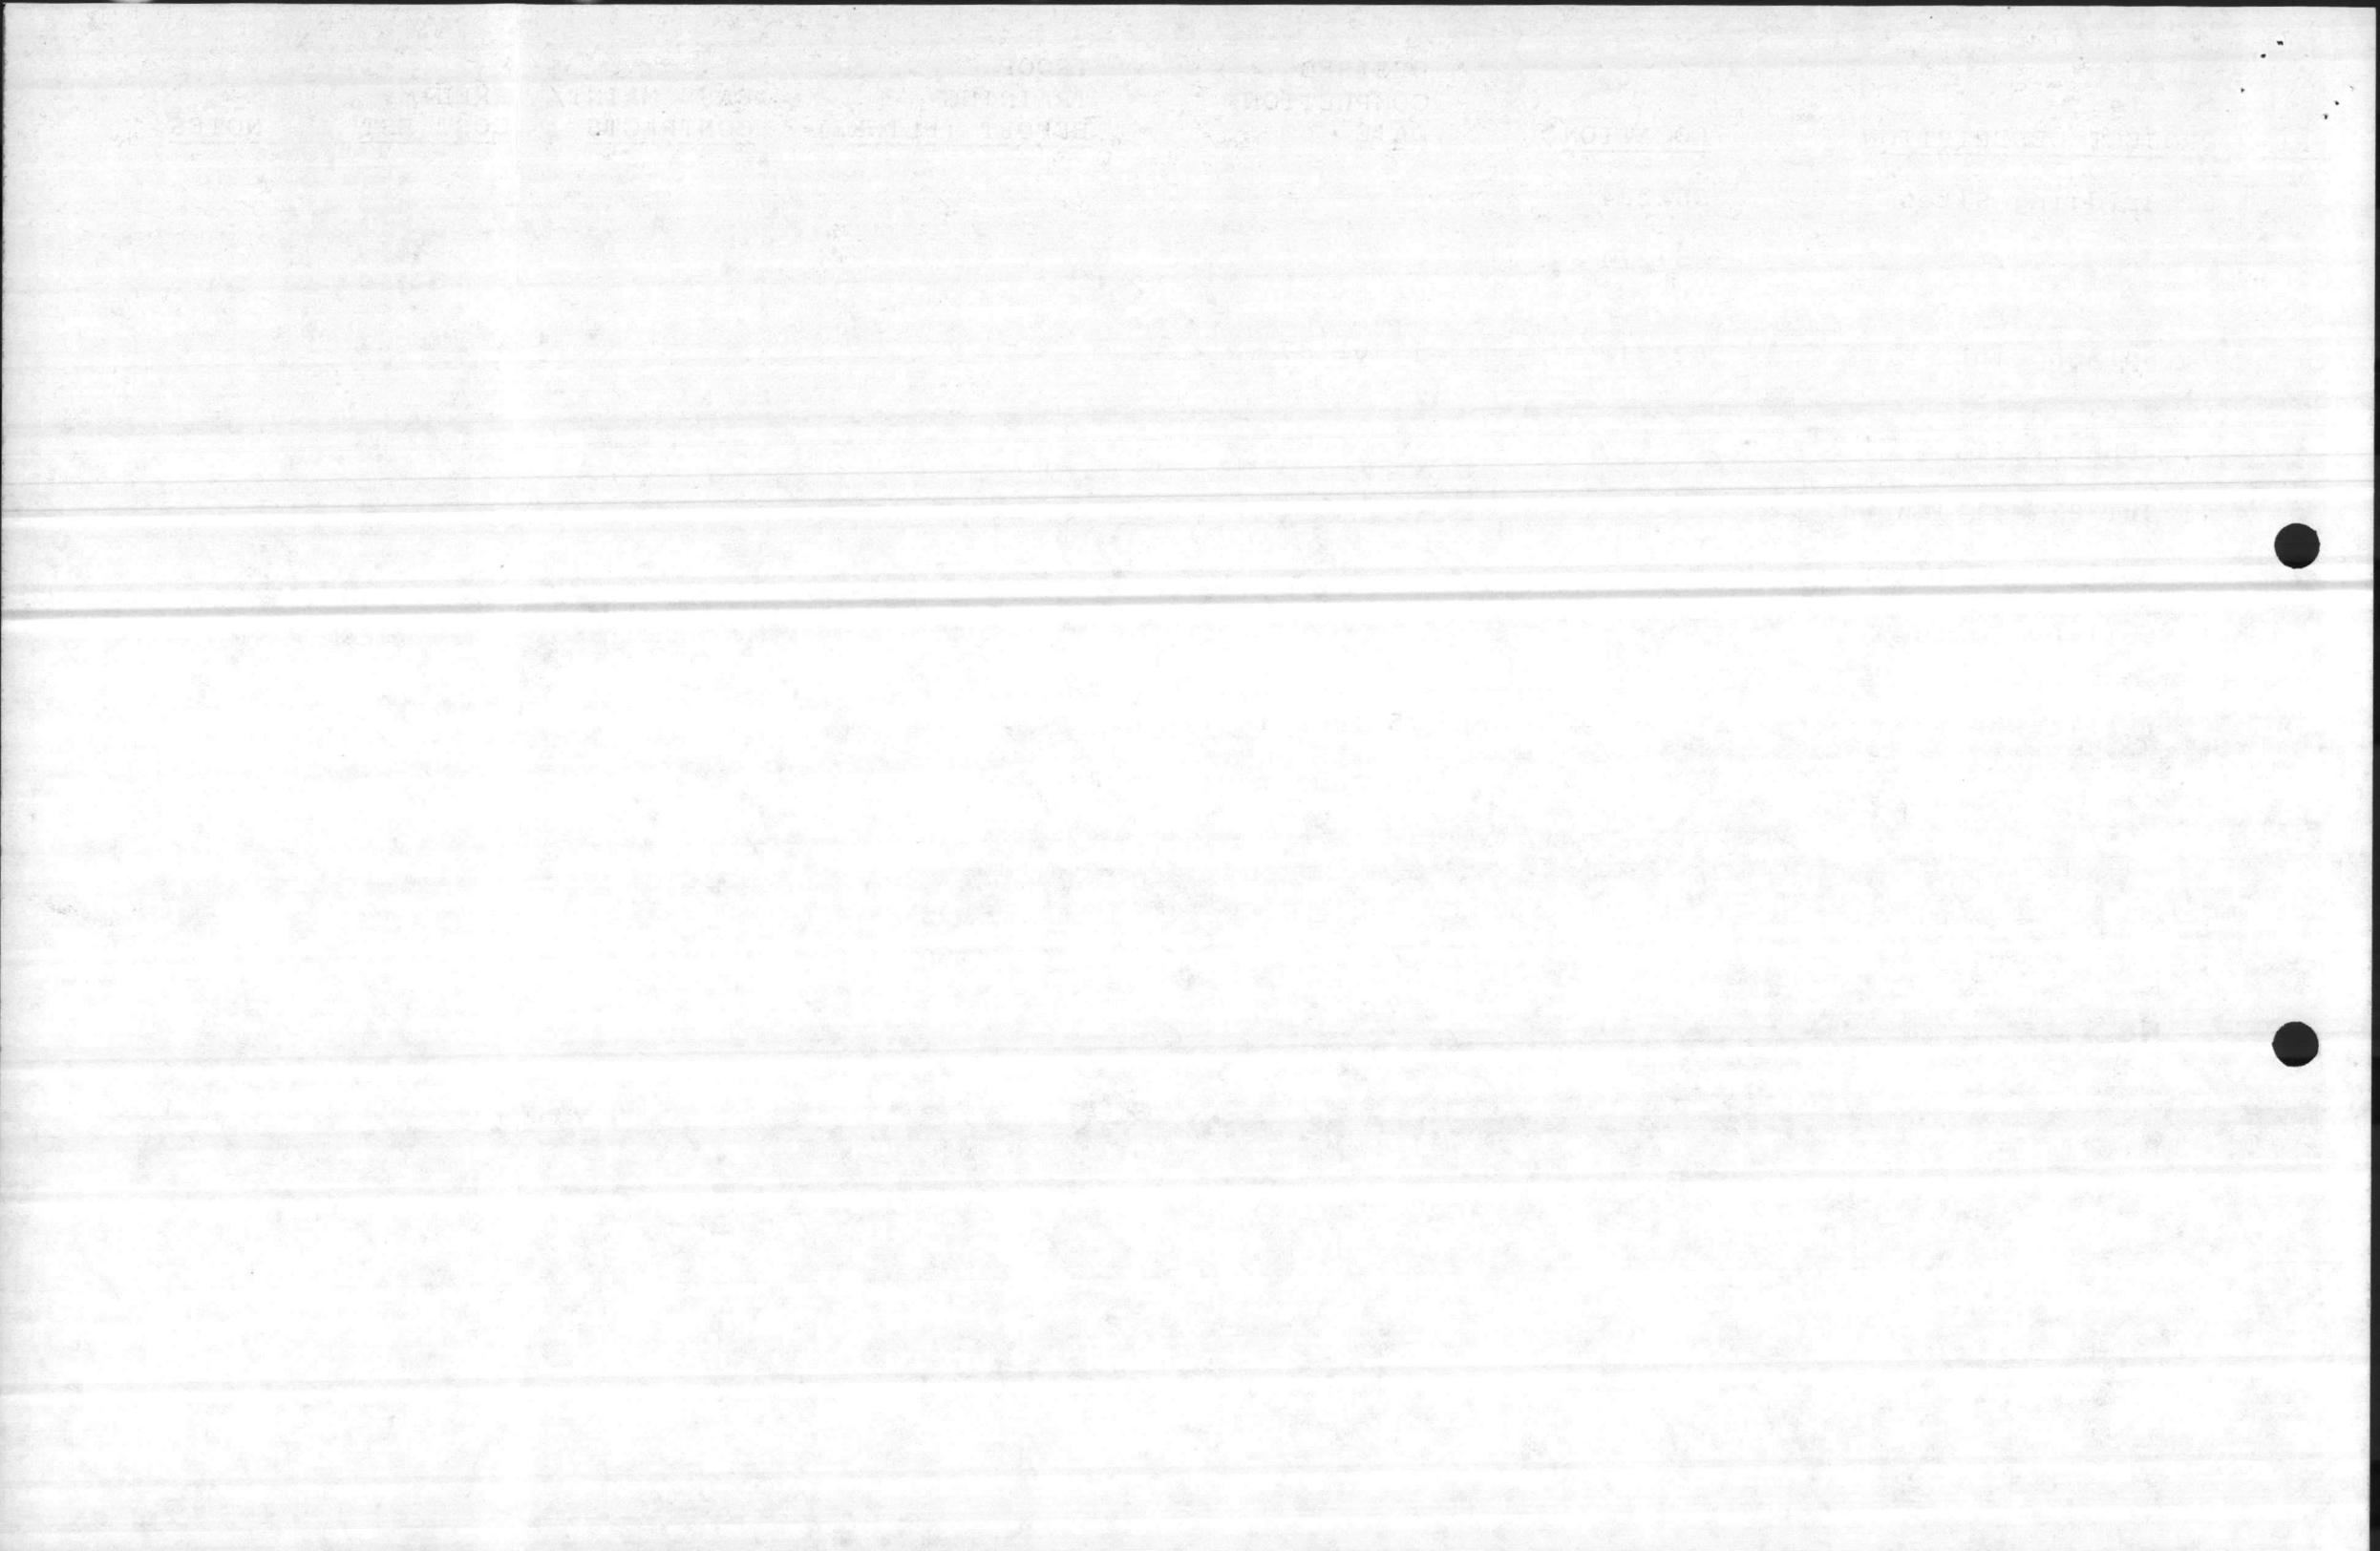


<u>PRI</u>	<u>PROJECT DESCRIPTION</u>	<u>LOCATION</u>	<u>DESIRED COMPLETION DATE</u>	<u>TROOP TRAINING EFFORT (PLTWKS)</u>	<u>BASE MAINT/ CONTRACTS</u>	<u>PRELIM COST EST</u>	<u>NOTES</u>
	d. <u>PHASE IV</u>						
	(1 Jan 88 - 30 Sep 88)						
	1. Completion of pending projects		30 Sep 88				
	2. Splashpoint	843343	30 Sep 88				
2-86	G-4 Range Engineer Training Area (ETA)	FA Area					
	<u>PHASE I</u>						
	Head Facility	FA Area	FY 86	6-9 months	Base Maint (Elec SVC)	\$97,000	
	Classroom Annex	FA Area		2d CEB			
	Septic Tank/Leach Field						
	Water and Power Distribution						
	Personnel Bunkers	LZ Crow					
	ASP						
	Outdoor Classroom (1)						

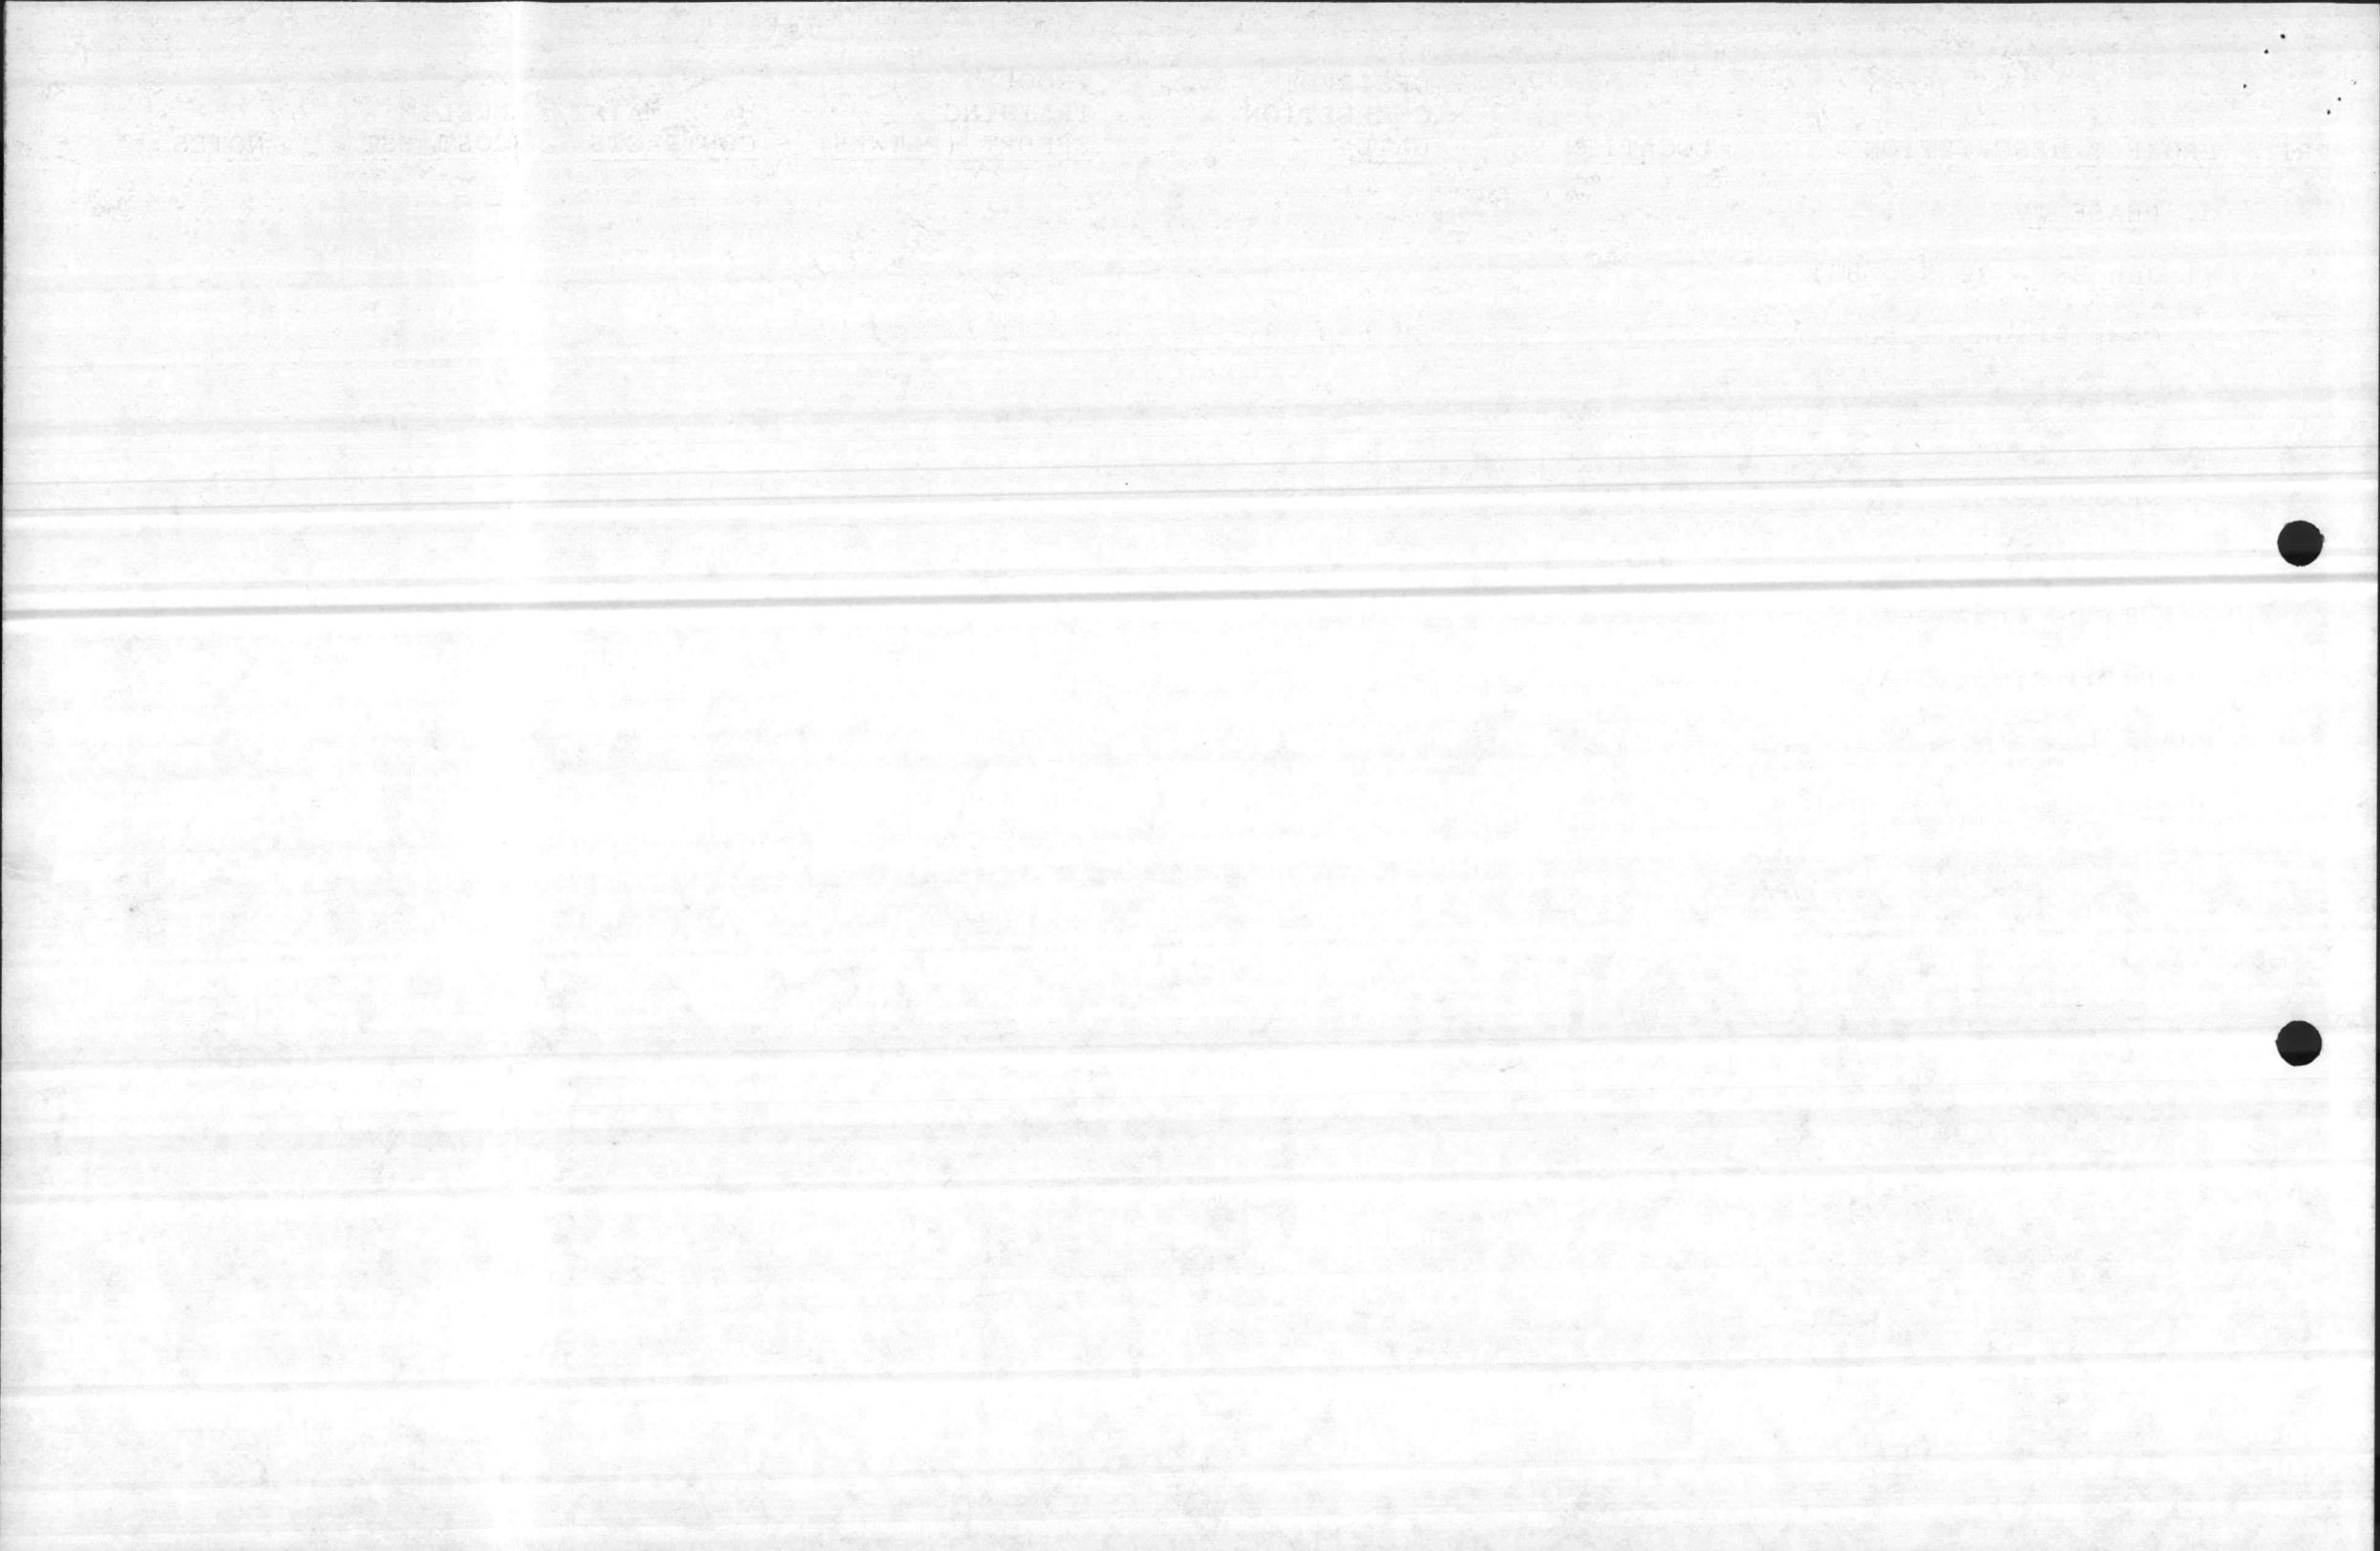


<u>PRI</u>	<u>PROJECT DESCRIPTION</u>	<u>LOCATION</u>	<u>DESIRED COMPLETION DATE</u>	<u>TROOP TRAINING EFFORT (PLTWKS)</u>	<u>BASE MAINT/ CONTRACTS</u>	<u>PRELIM COST EST</u>	<u>NOTES</u>
3-86	Bn Expeditionary Bivouac Sites K-Range	Verona Loop (near K303)	FY 86	2d CEB	Base Maint	\$18,000	
4-86	Area 2 "0" Course	Area 1/2	FY 86	N/A	2d FSSG	Unknown	
5-86	Rappelling Tower	French Creek	Jun 86	2d FSSG	N/A	Unknown	2d CEB to do i FSSG unable to take
6-86	LAV Firing Lanes Timber Harvest	G5/G7	FY 86	Troop Training Range Const	N/A	\$7,000	
7-86	G6 Range Upgrade (wire/electric)	G6	FY 86	N/A	Contract/ Base Maint	Unknown	Currently unde contract
8-86	<u>New Arty Positions Sites</u>						
	GP 31 (New) (Pri 1)	VIC 892267					
	GP 39 (New) (Pri 2)	VIC 854300					

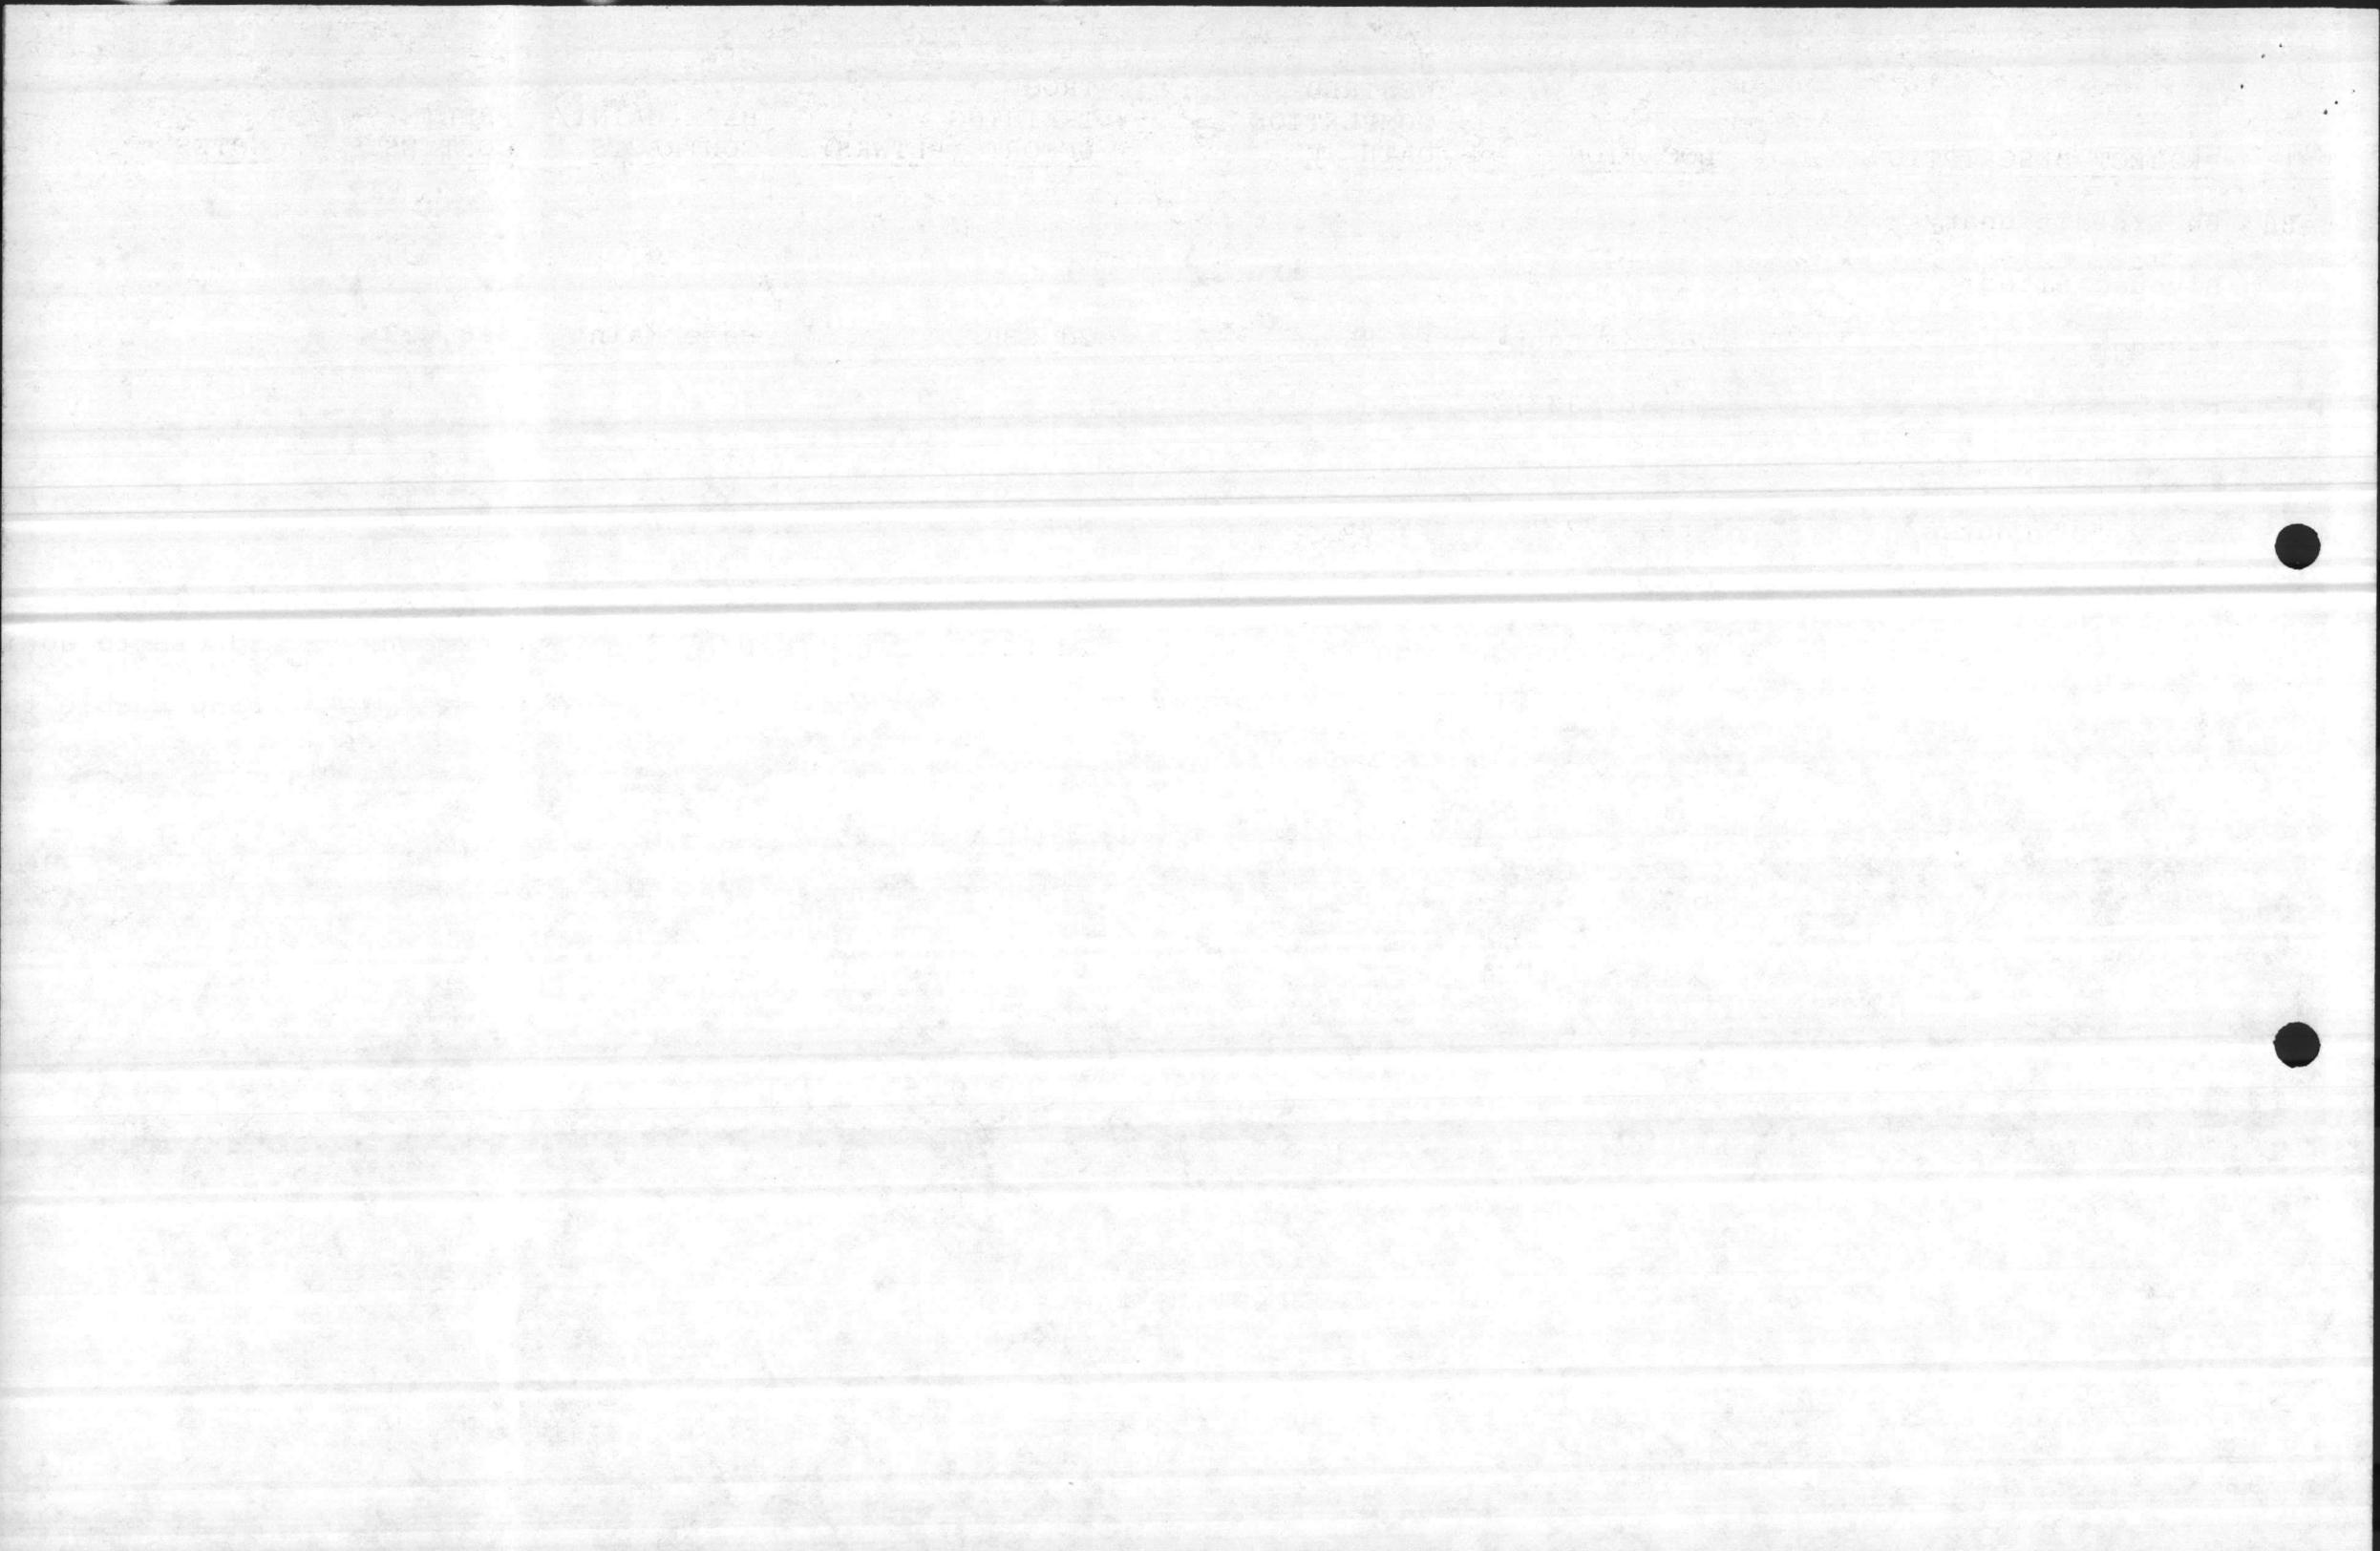


<u>PRI</u>	<u>PROJECT DESCRIPTION</u>	<u>LOCATION</u>	<u>DESIRED COMPLETION DATE</u>	<u>TROOP TRAINING EFFORT (PLTWKS)</u>	<u>BASE MAINT/ CONTRACTS</u>	<u>PRELIM COST EST</u>	<u>NOTES</u>
8-86 (Cont)	GP 34 (New) (Pri 3)	VIC 807311					
	GP 2 (New) (Pri 4)	VIC 938404			2d CEB (Partial)		Replaces curre GP 2
	GP 5 (New) (Pri 5)	VIC 944413					Replaces curre GP 5
	GP 42 (Pri 6)	VIC 853322					
	GP 22 (Pri 7))	VIC 877294					Replaces curre GP 22

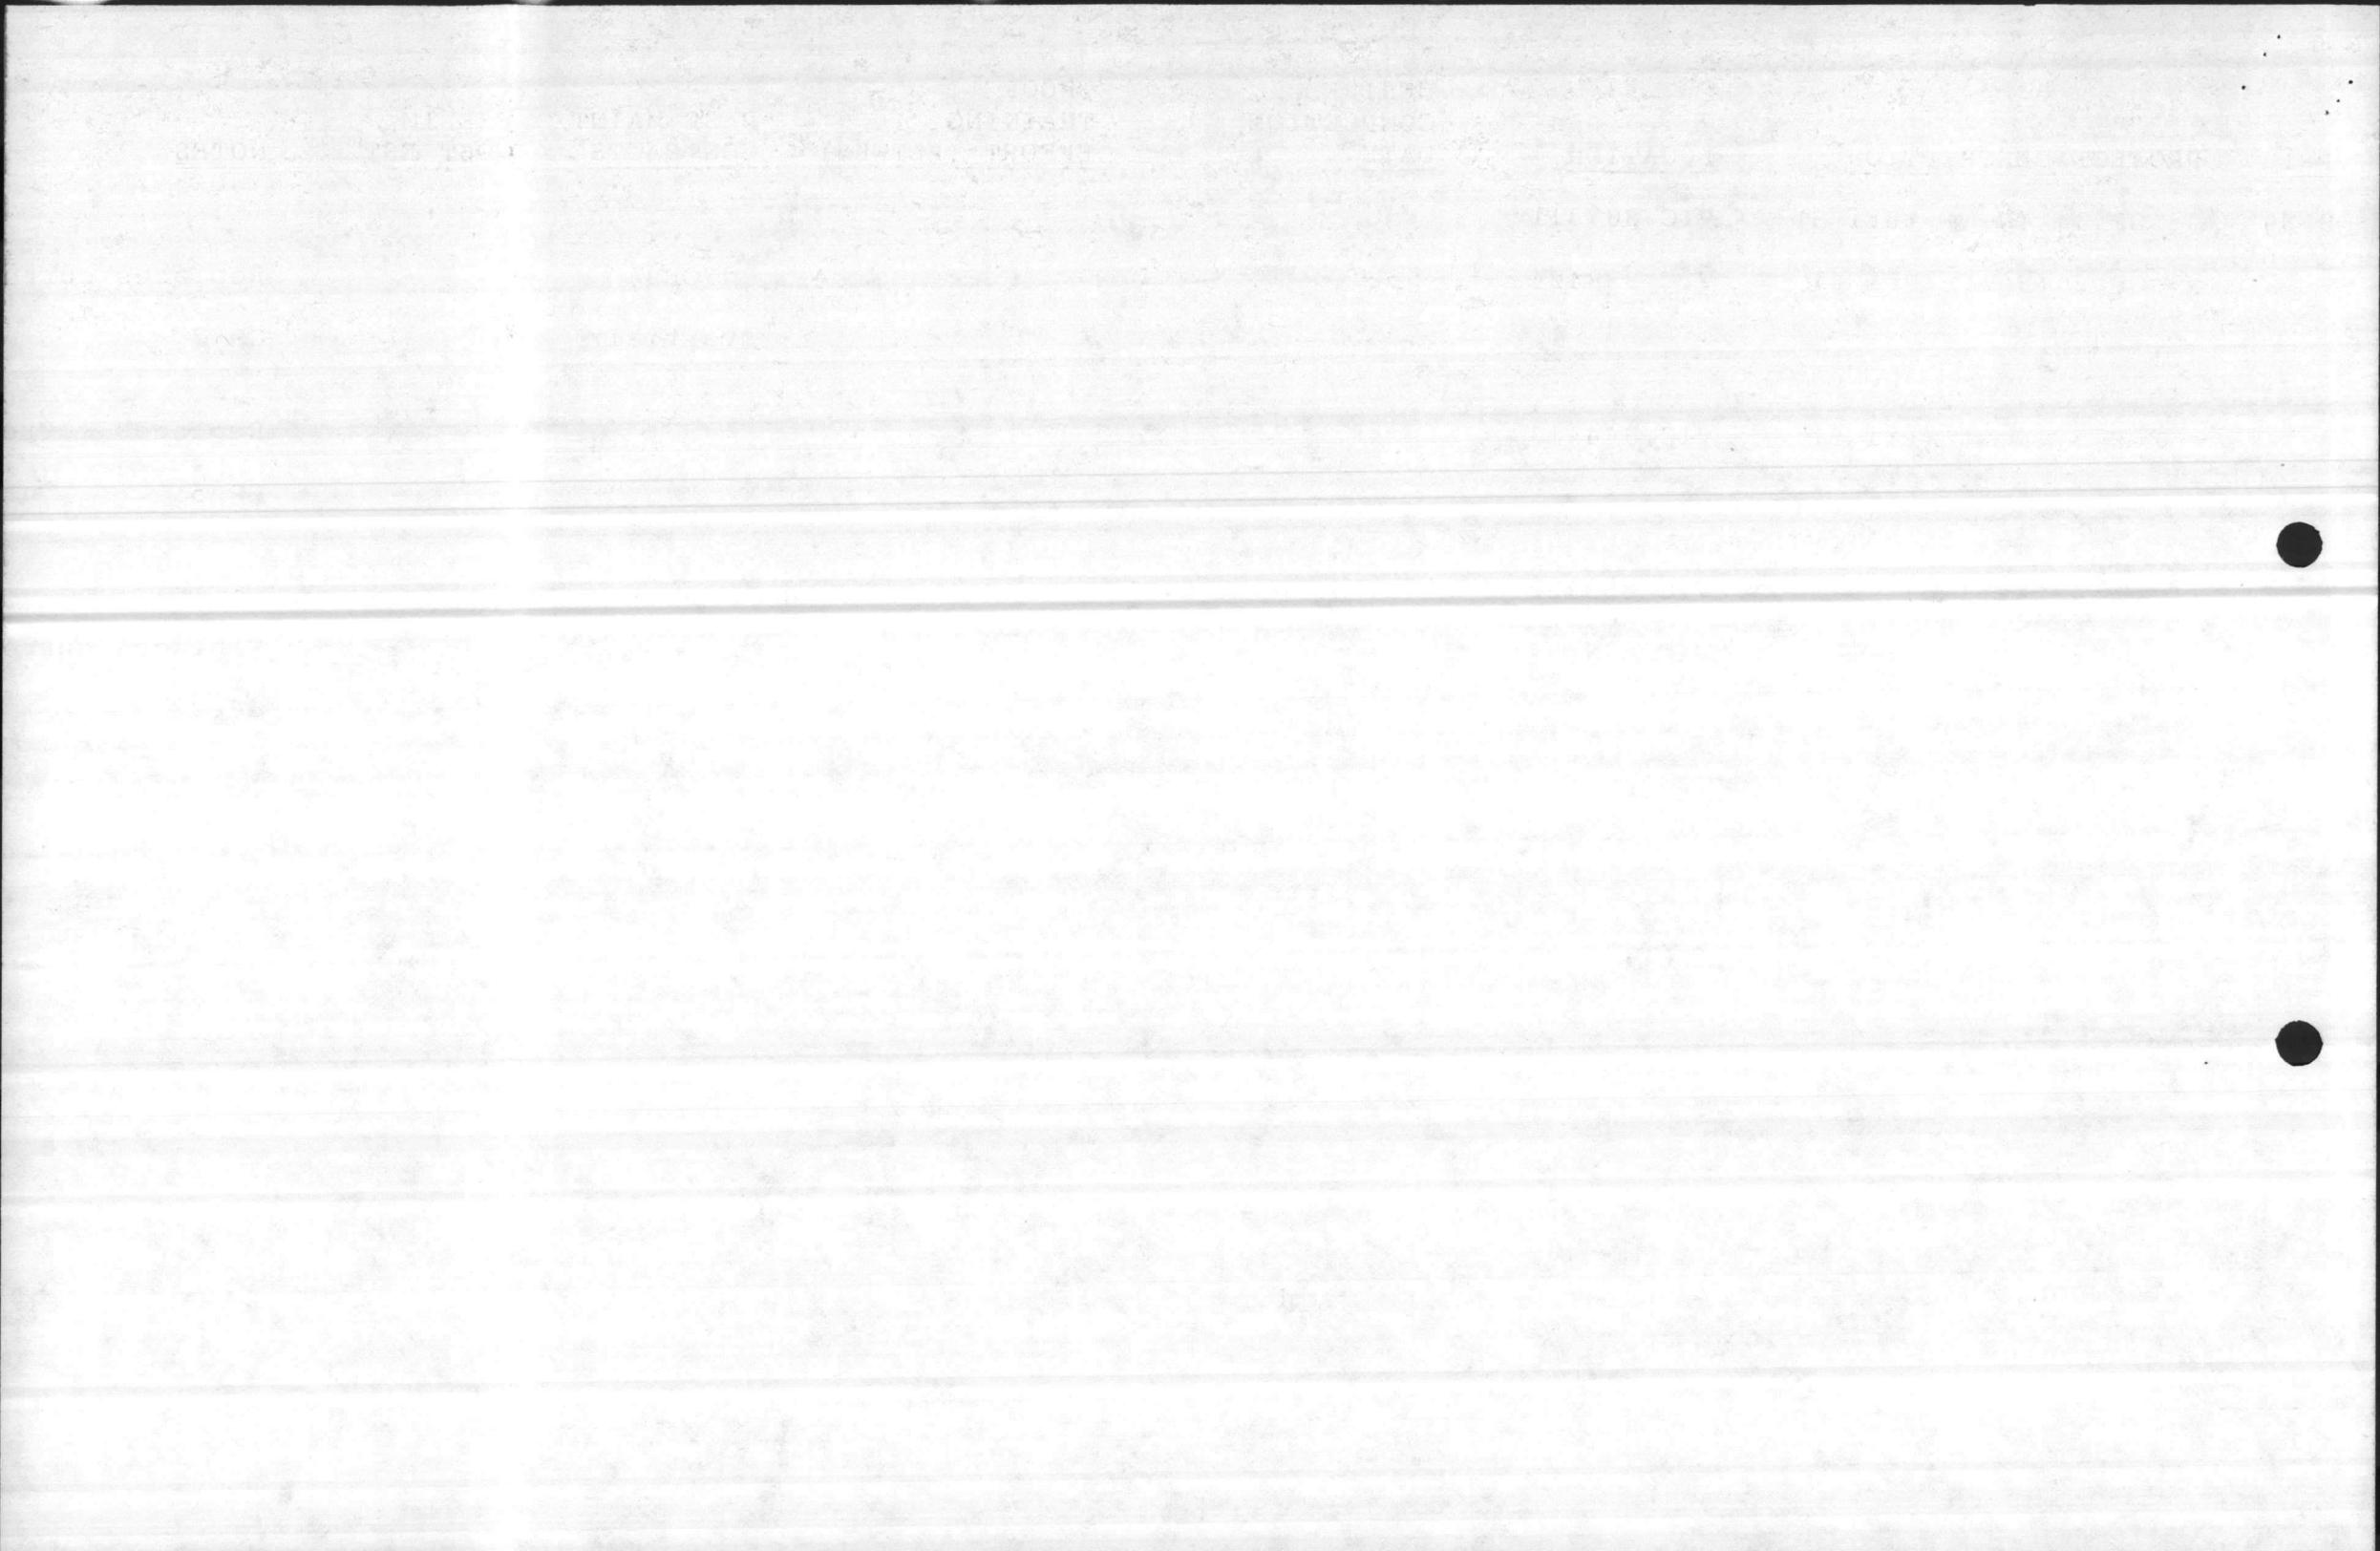


<u>PRI</u>	<u>PROJECT DESCRIPTION</u>	<u>DESIRED LOCATION</u>	<u>TROOP COMPLETION DATE</u>	<u>TRAINING EFFORT (PLTWKS)</u>	<u>BASE MAINT/ CONTRACTS</u>	<u>PRELIM COST EST</u>	<u>NOTES</u>
	<u>PHASE II ETA</u>						
1-87	Messhall (1)						
	Classroom		FY 87	6 months	N/A	\$86,000	
	Outdoor Classroom		FY 87	2d CEB			
	Mess Shed		FY 87				
2-87	G-10 Range Expansion		31 Dec 87				See CO, 10th M letter 11019, Jan 86
	<u>PHASE I</u>						
	(1 Oct 87 - 31 Dec 87)						
	1. Timber Harvest/clear impact area	Top half of expan area in G-10					
	2. Timber Harvest/clear observation area for 4 mobile OP course stations	Station sites #8,#7,#6,#5					Priority: Sta 8 Sta 7 Sta 6 Sta 5

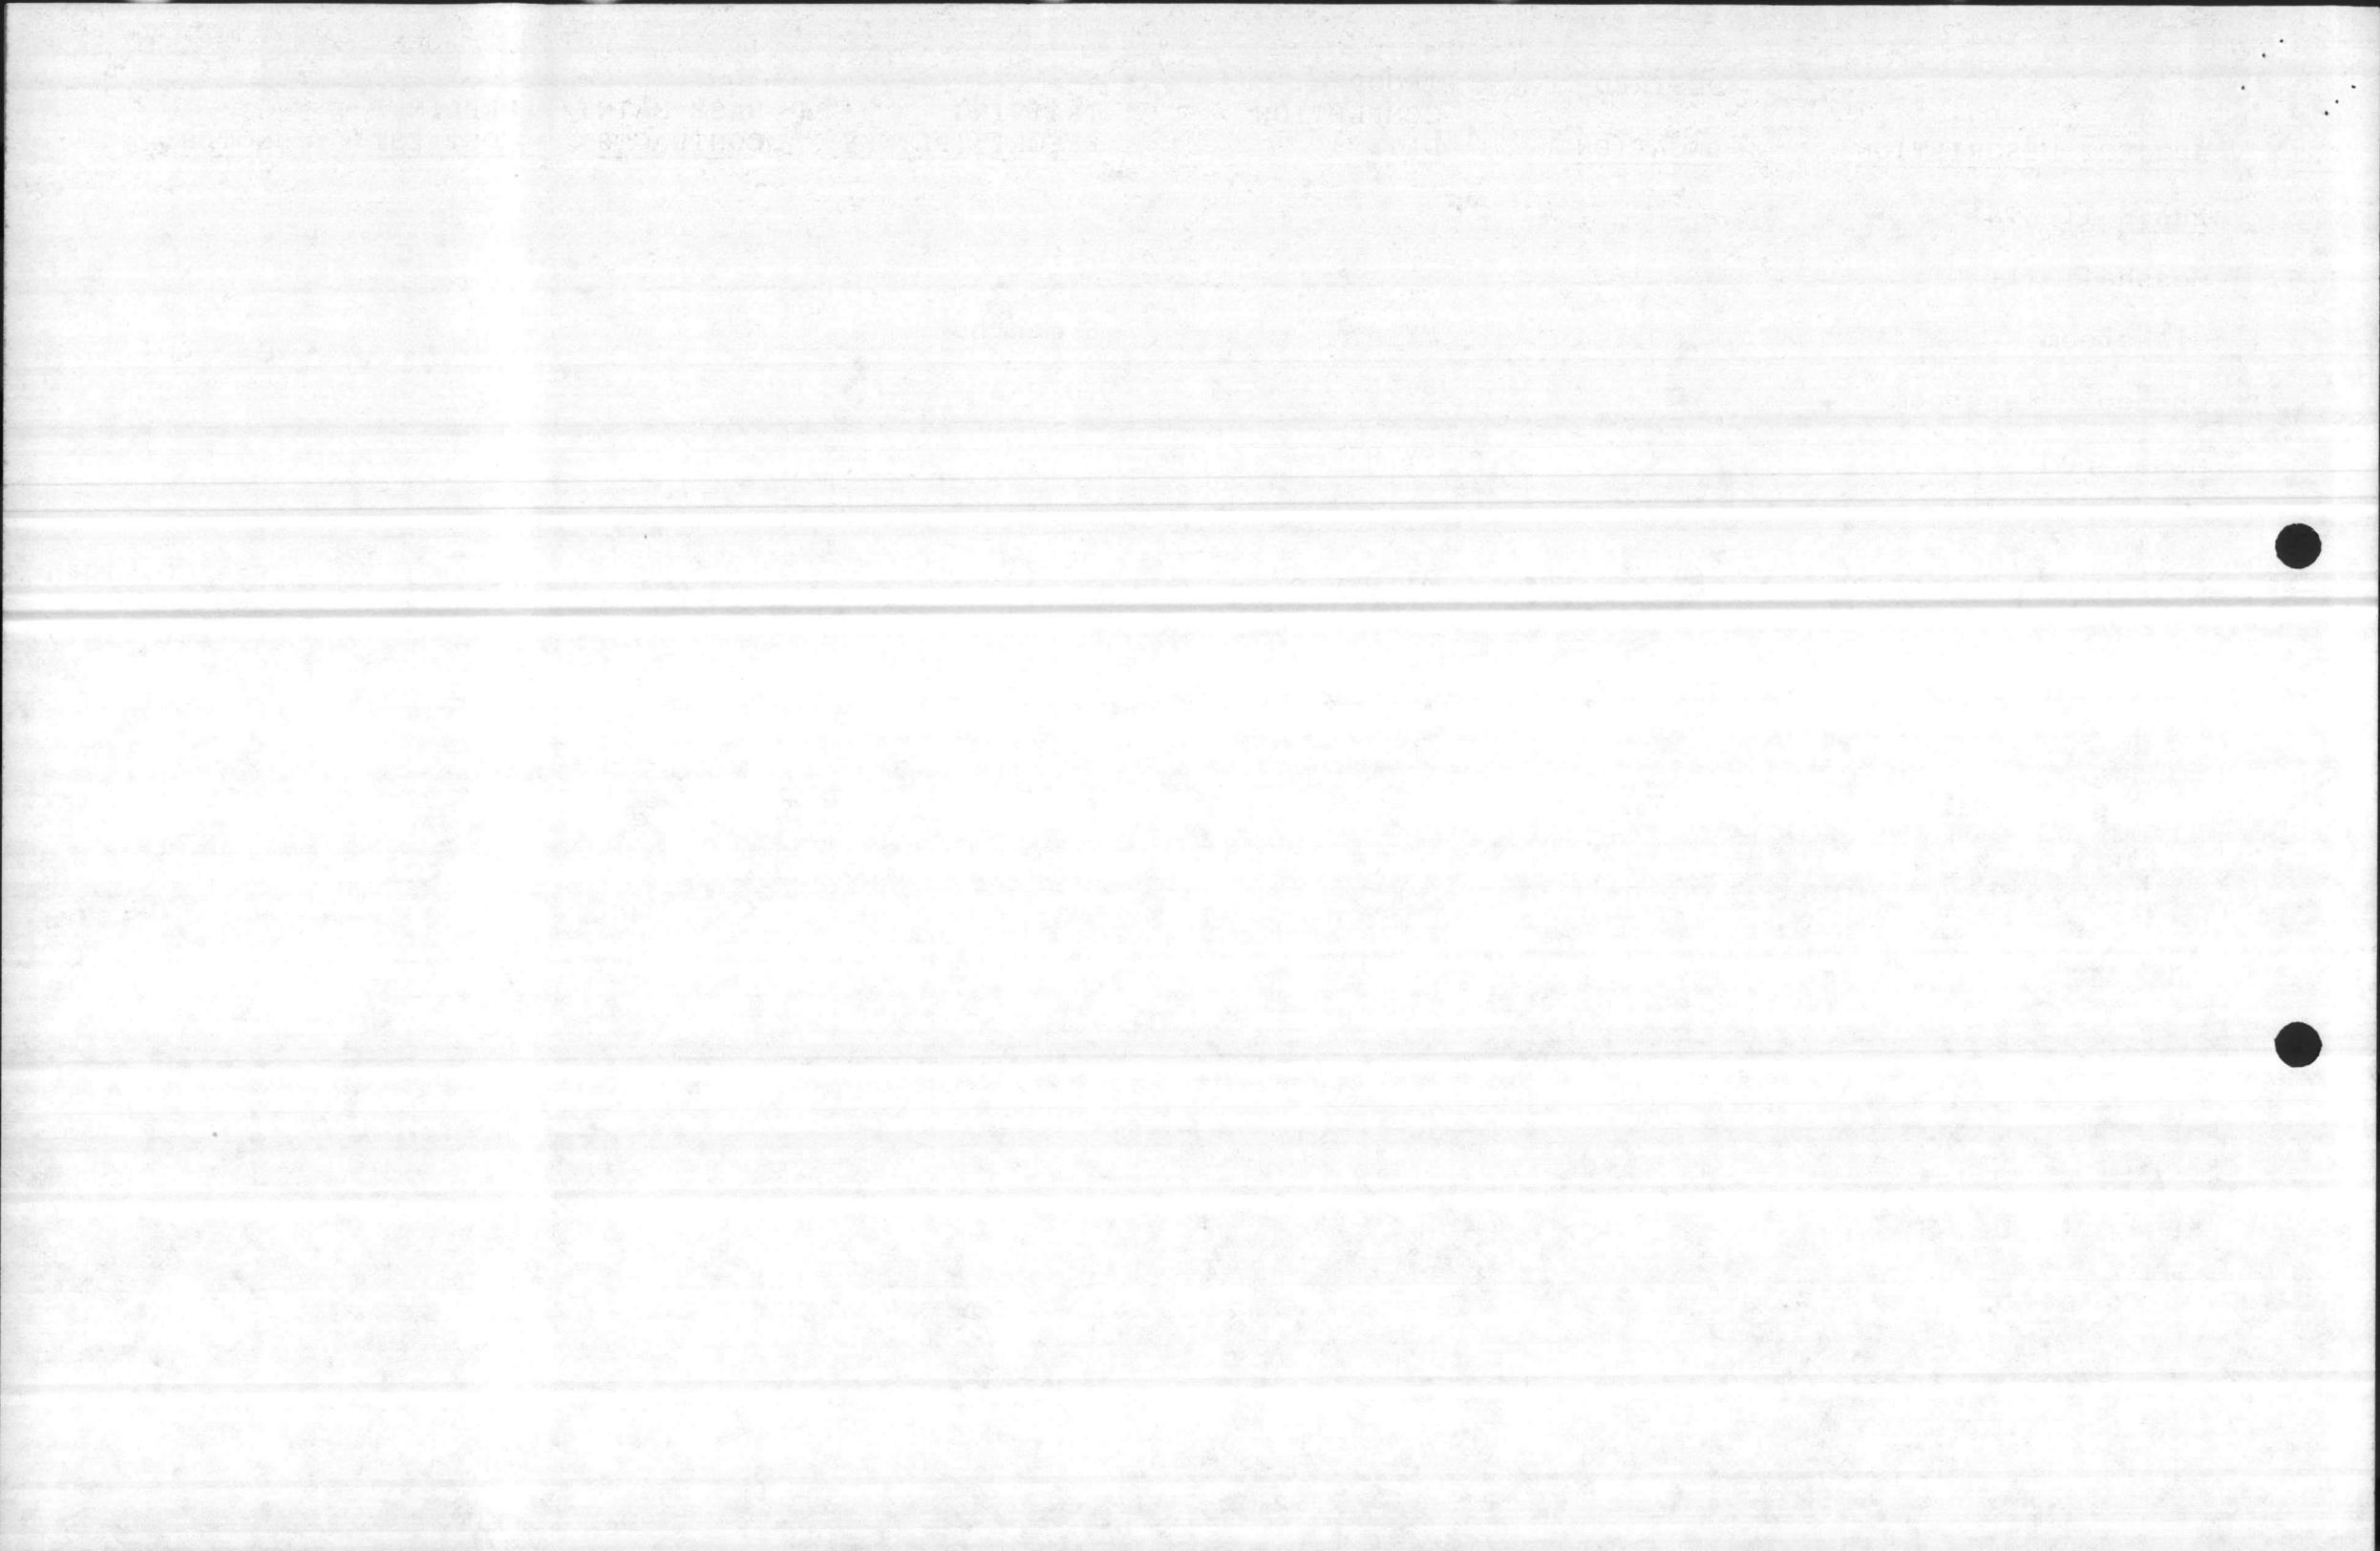


<u>PRI</u>	<u>PROJECT DESCRIPTION</u>	<u>LOCATION</u>	<u>DESIRED COMPLETION DATE</u>	<u>TROOP TRAINING EFFORT (PLTWKS)</u>	<u>BASE MAINT/ CONTRACTS</u>	<u>PRELIM COST EST</u>	<u>NOTES</u>
3-87 (cont)	3. Upgrade tank trails	From OP3 to OP5		Unknown	Base Maint		
	4. Construct Barriers on downrange trails coincident with proj a.2 above						
	5. Construct bunker for indirect fire training	G-10 (Specific LOCA unk)	50% by 31 Dec 87	2d CEB		10-20K	
	G-10 Range Expansion						
	<u>PHASE II</u>						
	(1 Jan 87 - 31 Mar 87)						
	1. Timber Harvest/clear impact area	Bottom half expan area in G-10					
	2. Timber Harvest/clear observation areas for 4 mobile OP course station	Station sites #4-#1	31 Mar 87				Priority: Sta 4, Sta 3 Sta 2, Sta 1

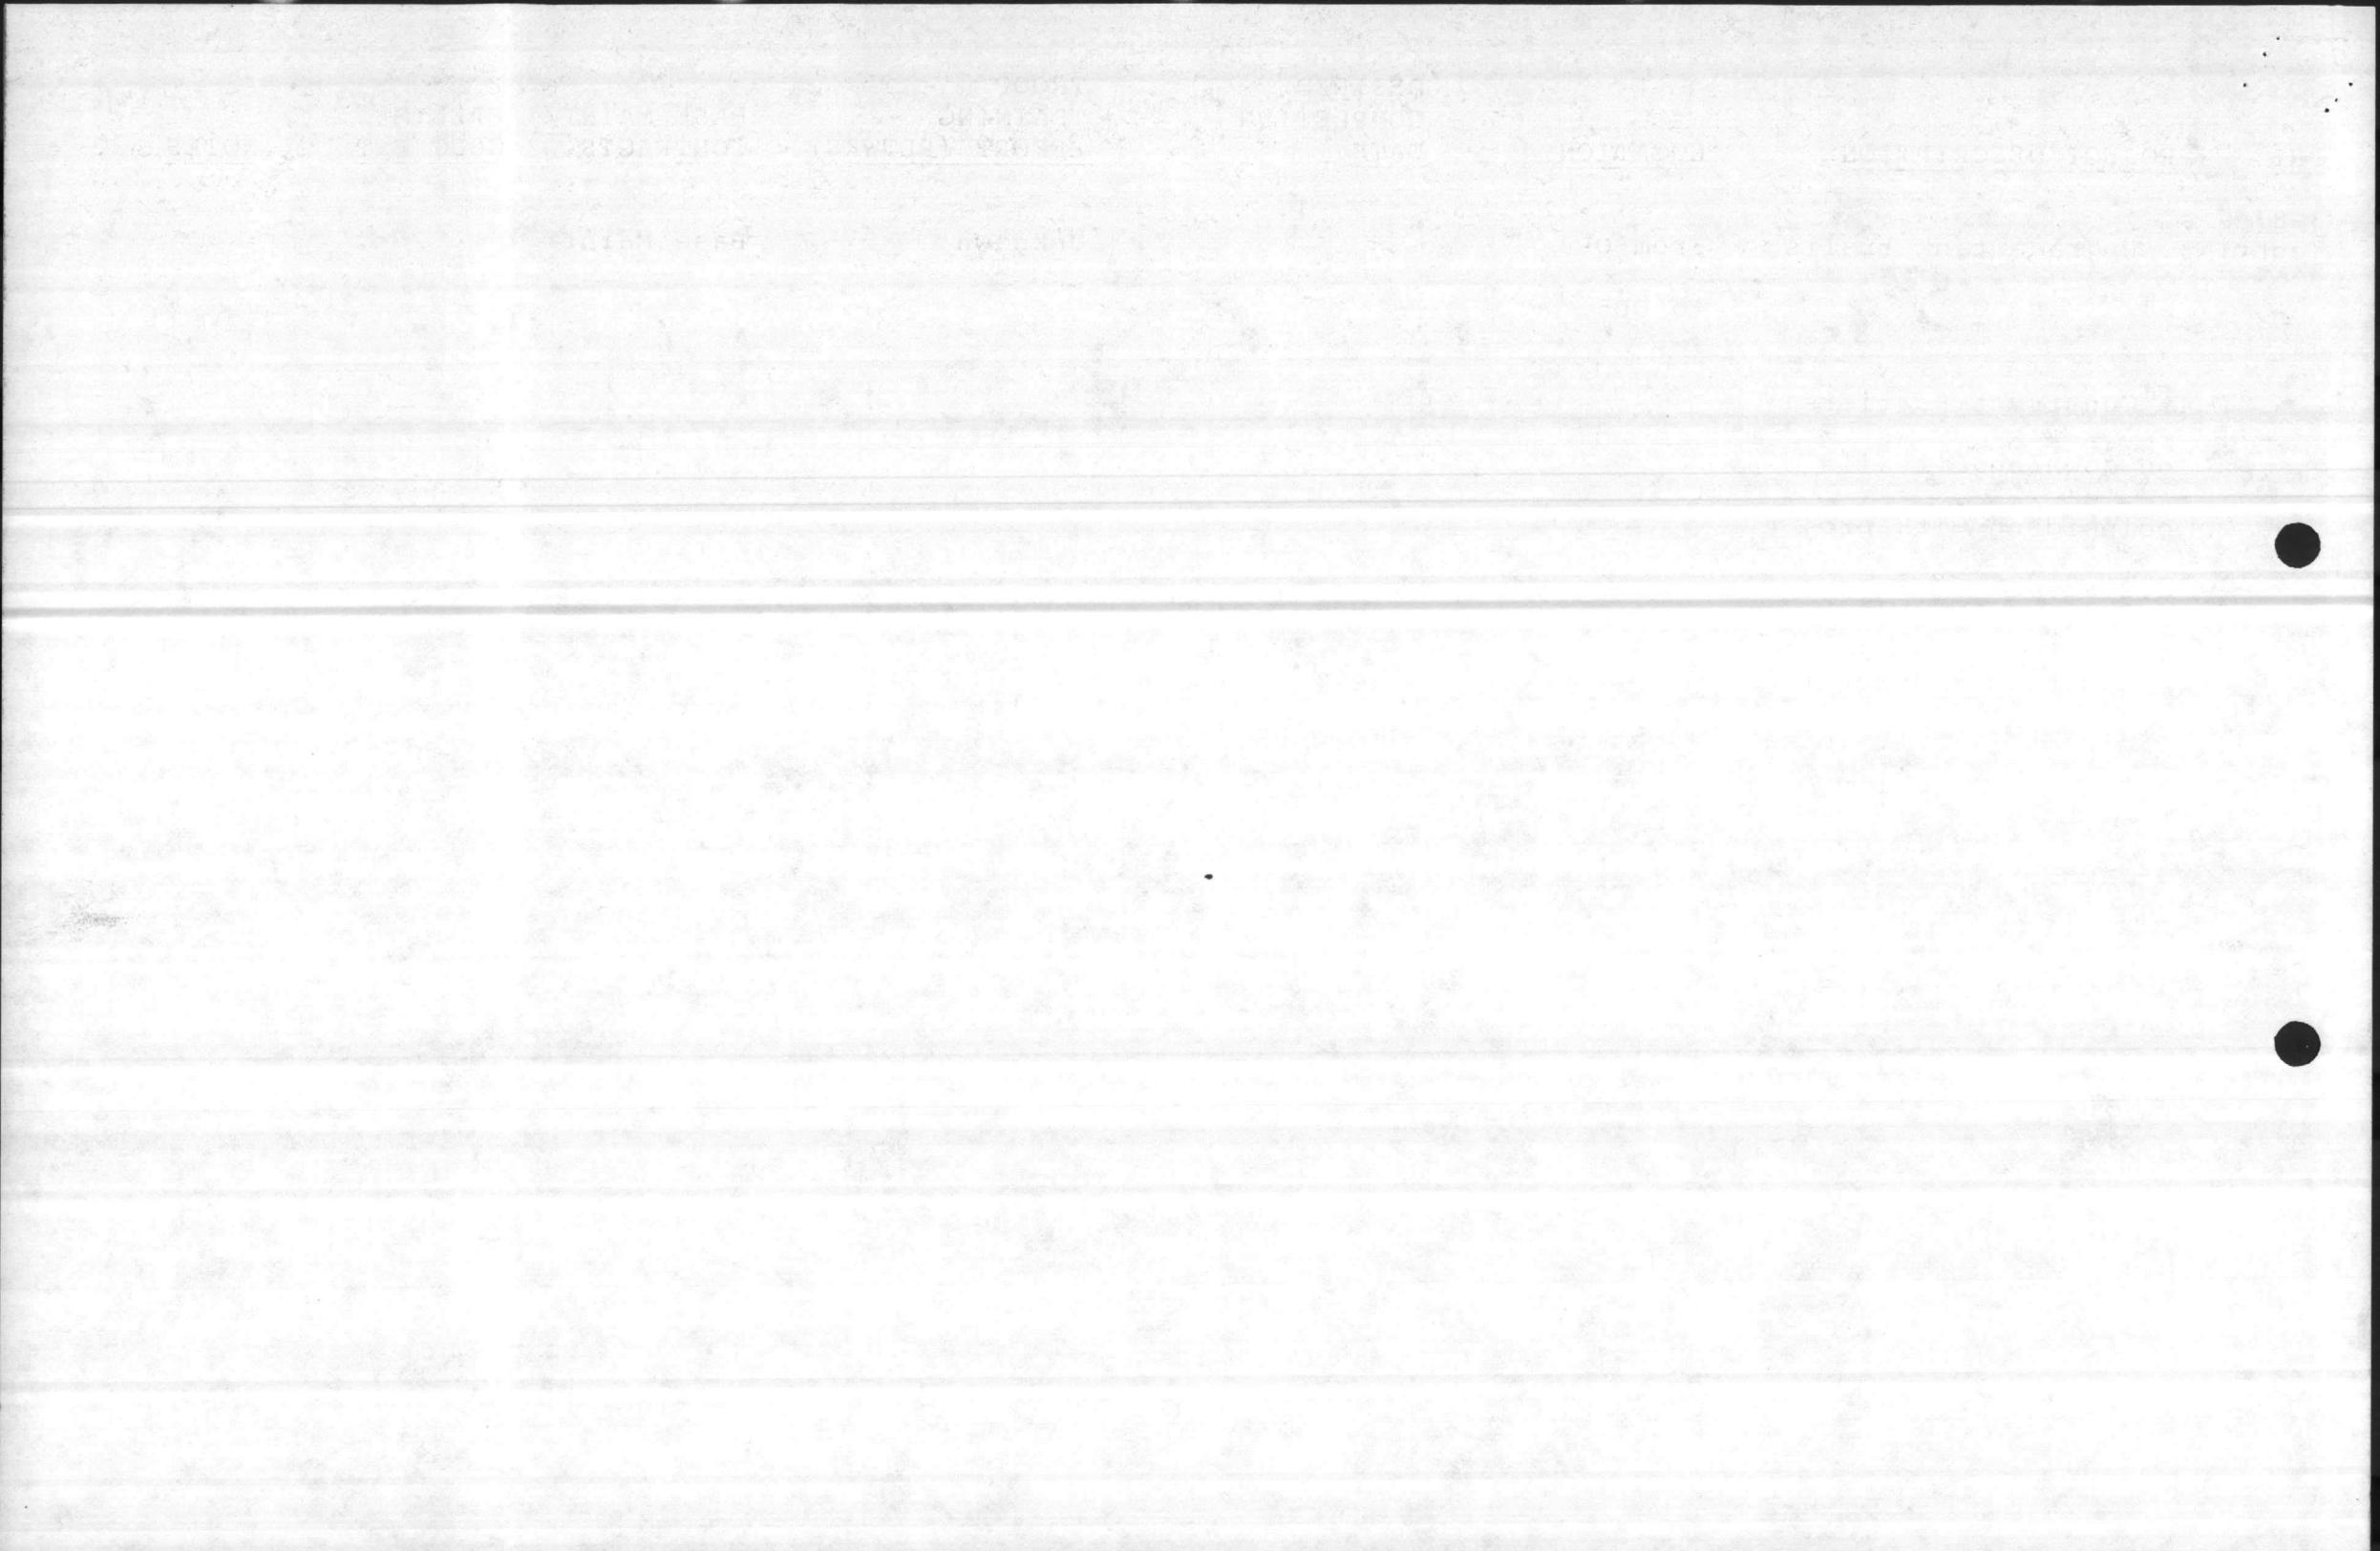


<u>PRI</u>	<u>PROJECT DESCRIPTION</u>	<u>LOCATION</u>	<u>DESIRED COMPLETION DATE</u>	<u>TROOP TRAINING EFFORT (PLTWKS)</u>	<u>BASE MAINT/ CONTRACTS</u>	<u>PRELIM COST EST</u>	<u>NOTES</u>
3-87 (Cont)	3. Upgrade tank trails	From OP5 to sta 5					
	4. Construct barriers on downrange trails						
	5. Construct bunker for indirect fire training	G-10 (Specific LOCA unk)	100% by 31 Mar 87	4 wks		\$15,000	
	G-10 Range Expansion						
	<u>PHASE III</u>						
	(1 Apr 87 - 30 Sep 87)						
	1. Timber Harvest/clear impact area	Any residual areas in G-10	30 Jun 87				
	2. Timber Harvest/clear observation area for mobile op course stations	Any residual areas in G-10	30 Jun 87				
	3. Upgrade tank trails	From sta 5 to sta 1	30 Sep 87				

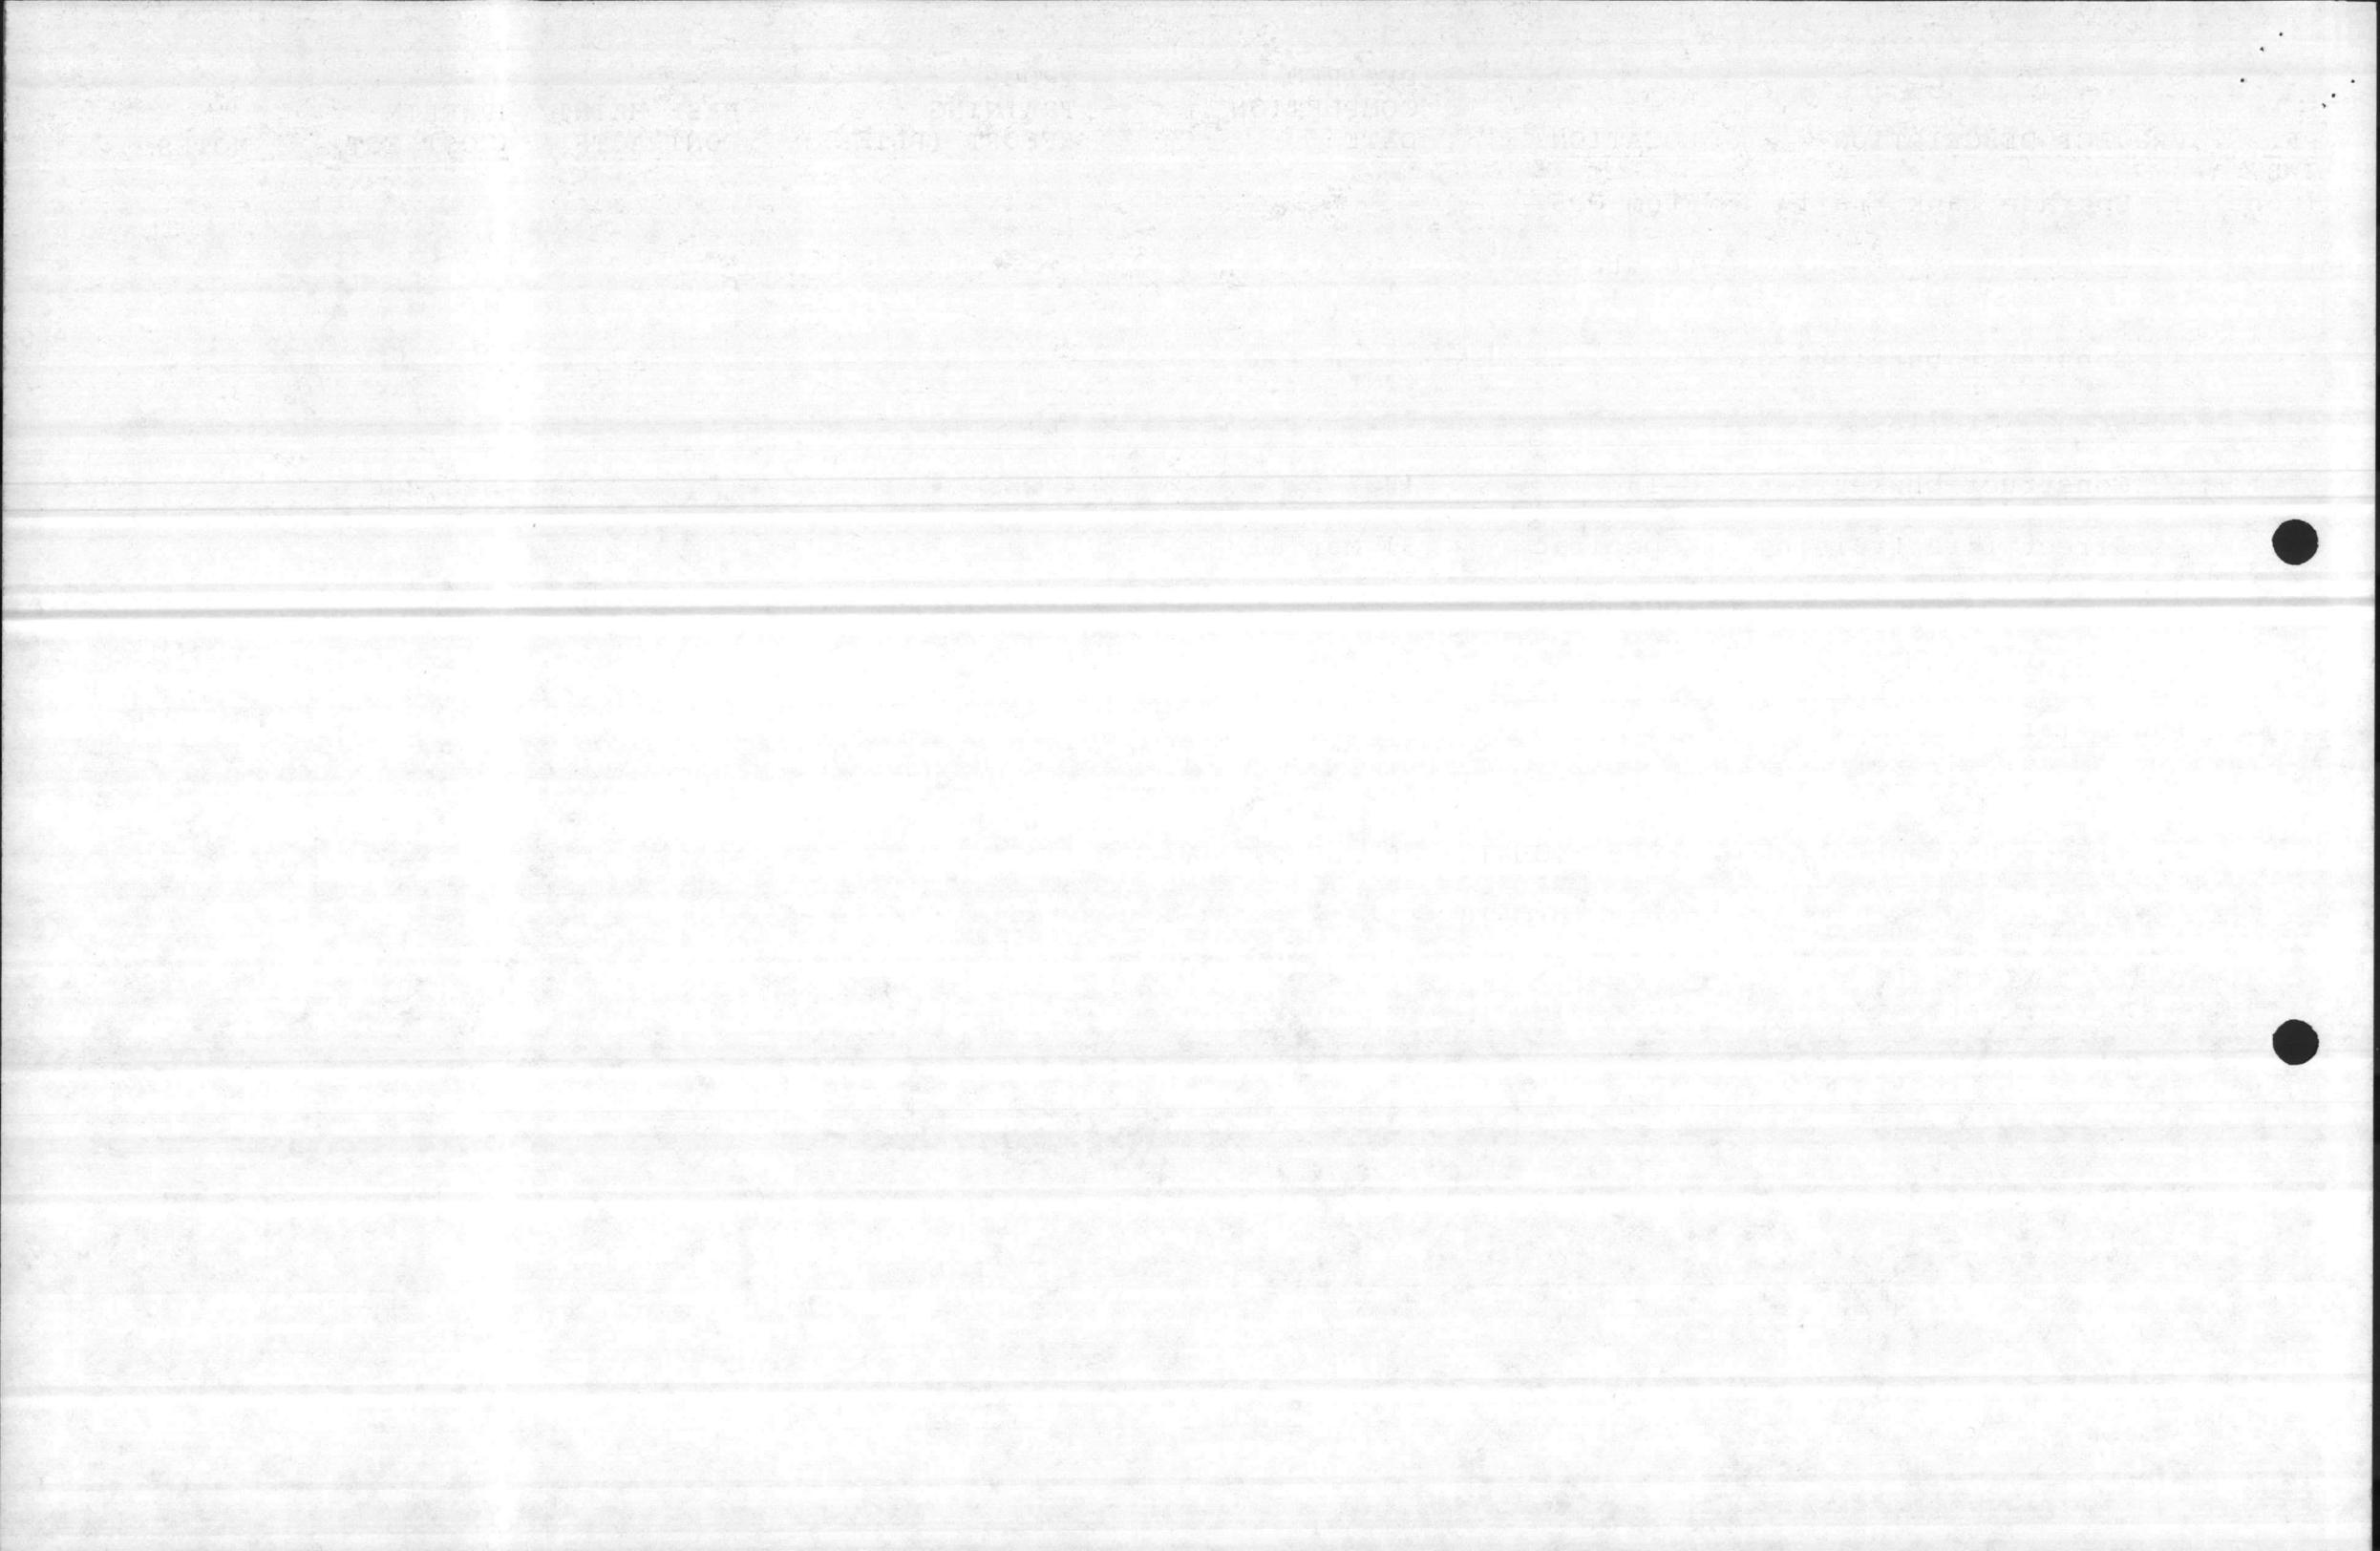


<u>PRI</u>	<u>PROJECT DESCRIPTION</u>	<u>LOCATION</u>	<u>DESIRED COMPLETION DATE</u>	<u>TROOP TRAINING EFFORT (PLTWKS)</u>	<u>BASE MAINT/ CONTRACTS</u>	<u>PRELIM COST EST</u>	<u>NOTES</u>
	4. Construct barriers on downrange trails						
	5. Combat Trails	VIC 943324 to VIC 919309	30 Sep 87				Permit uninhib access from G- TLZ Gooze inst of interruptin mobile OP cour
4-87	Expand/create artillery PSNS (complete)						
5-87	Bn Expeditionary Bivovac Sites						
	a. LZ Falcon/Gander Site	Falcon/Gander	FY 87	TBD	2d CEB	\$18,500	
	b. LZ Lark	LZ Lark	FY 87	TBD	2d CEB	\$18,500	
6-87	FCXC/F.O. Course Sub- caliber ORD (1/10 scale)	F-18		CEB			
	a. Tank Crossing PADS	VIC 874386					
	b. Combat trails	VIC 873393 to VIC 876383					

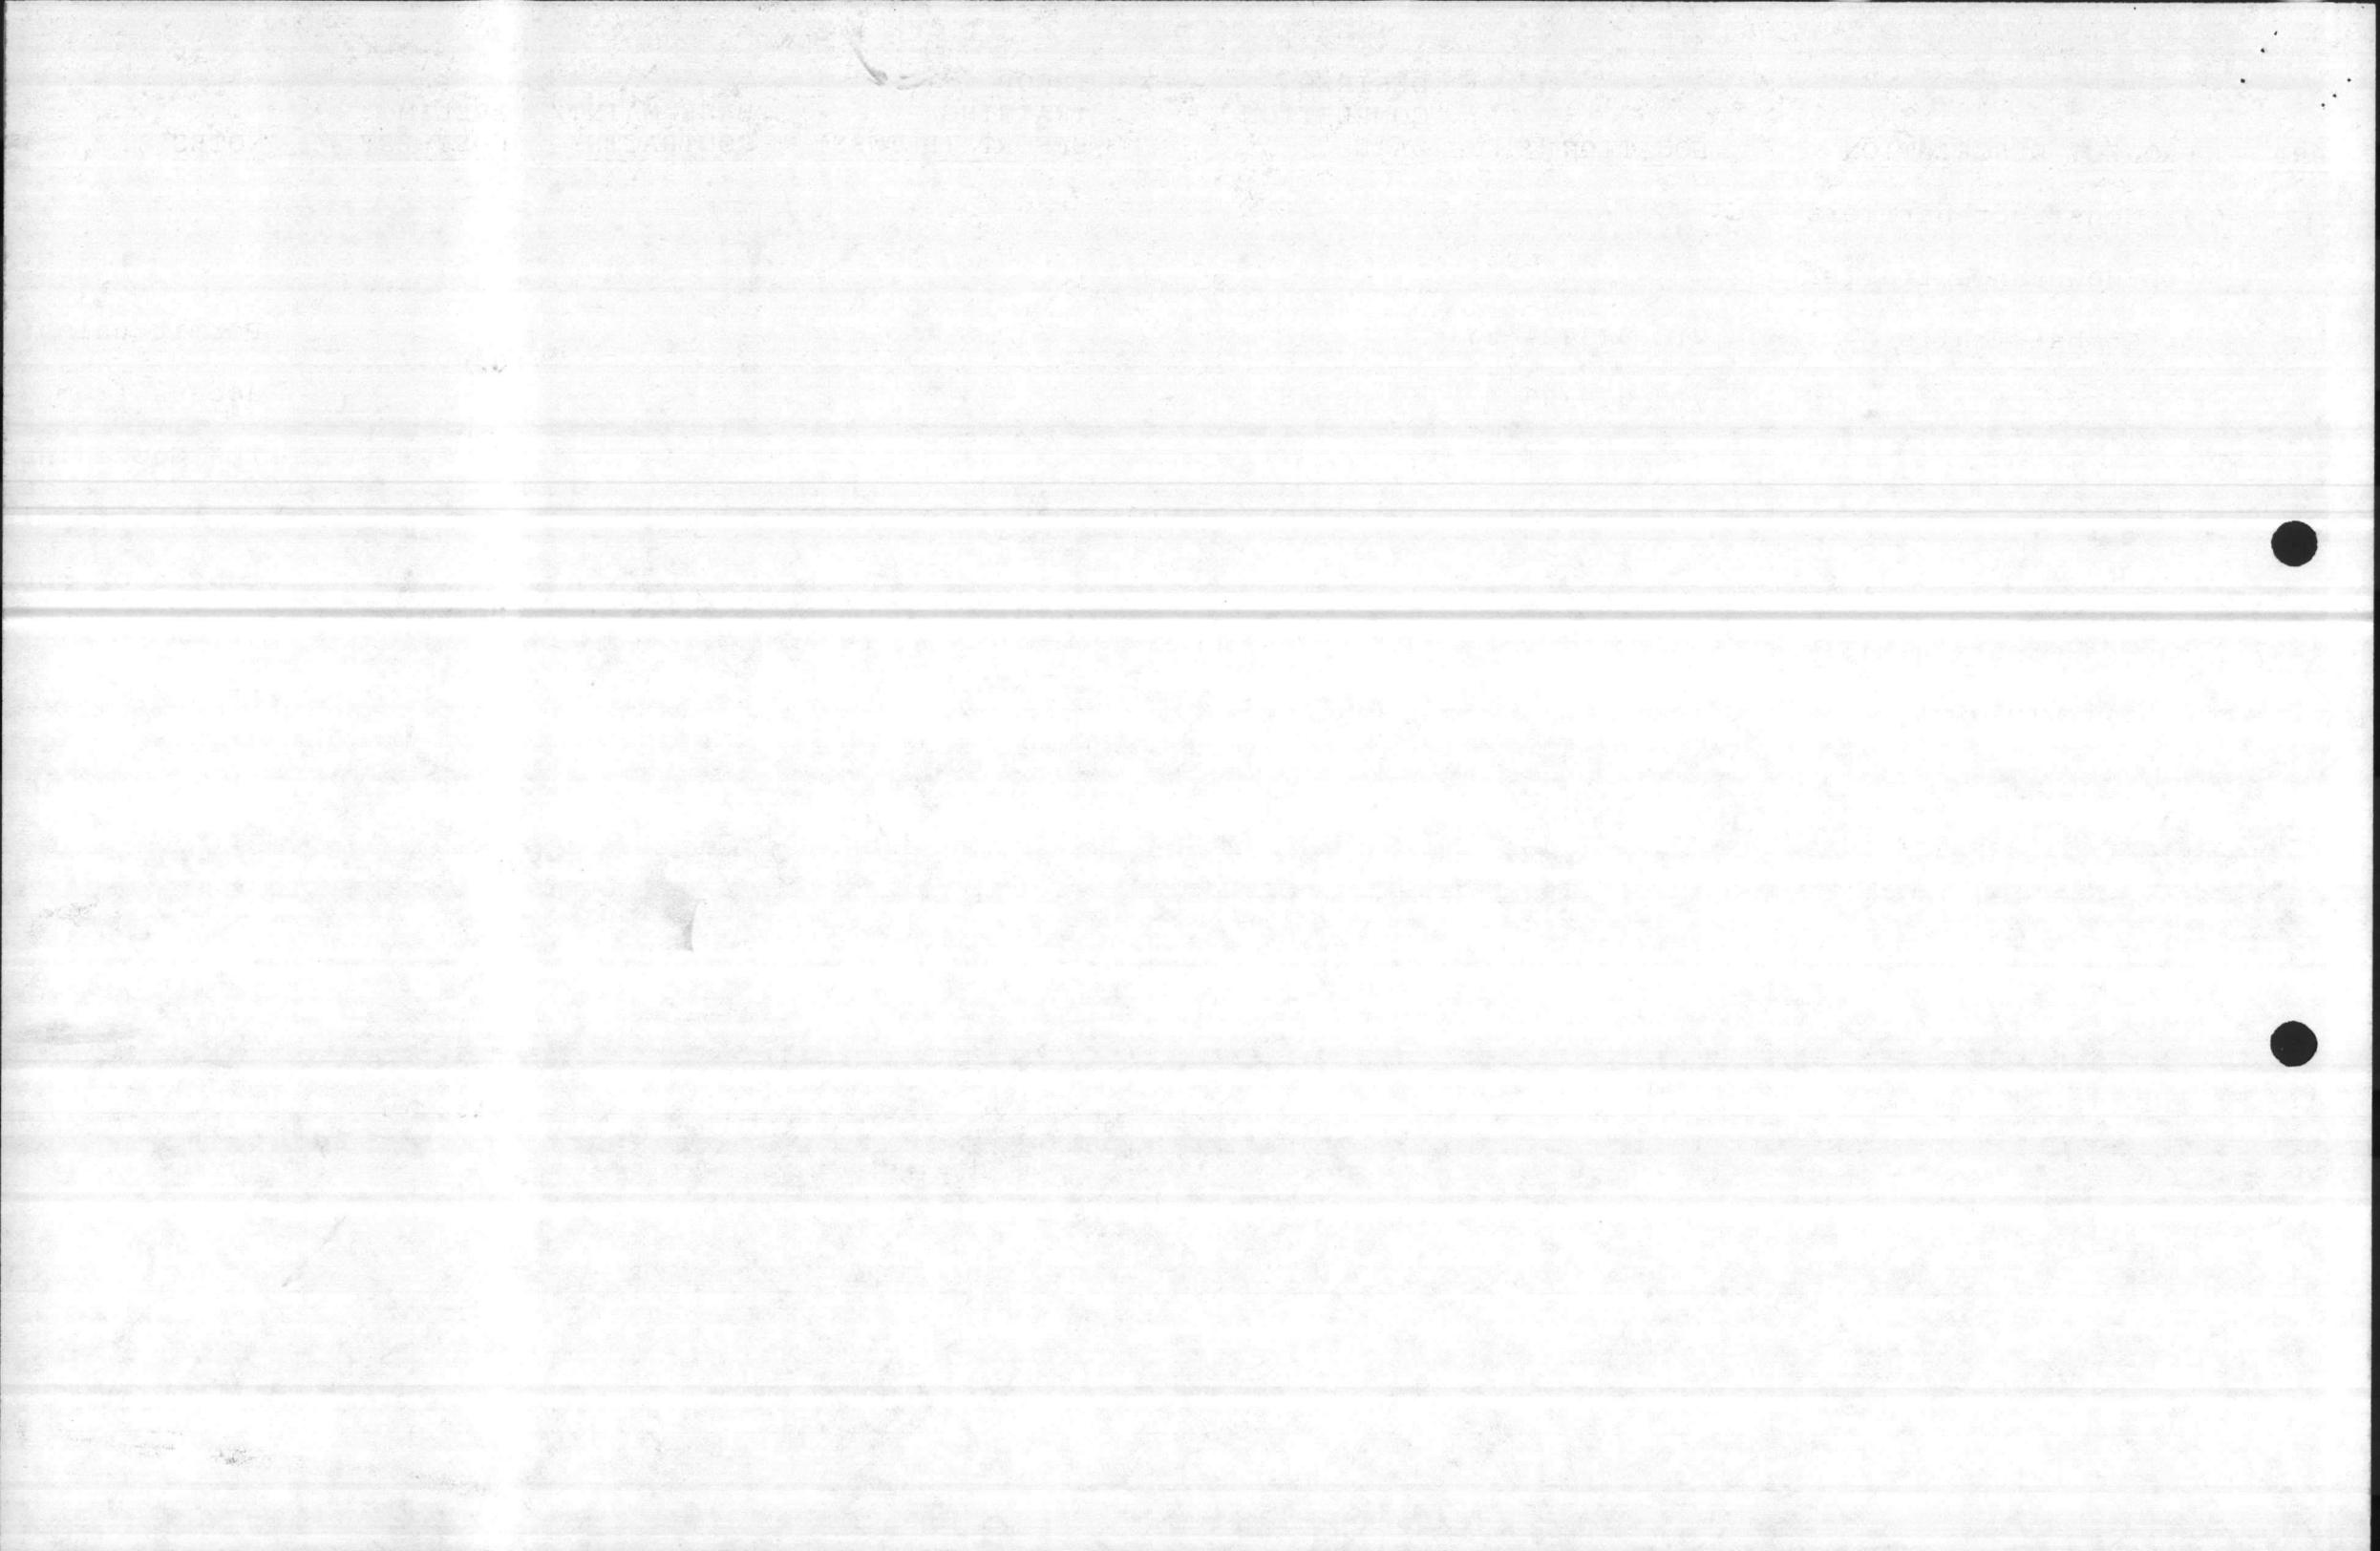


<u>PRI</u>	<u>PROJECT DESCRIPTION</u>	<u>LOCATION</u>	<u>DESIRED COMPLETION DATE</u>	<u>TROOP TRAINING EFFORT (PLTWKS)</u>	<u>BASE MAINT/ CONTRACTS</u>	<u>PRELIM COST EST</u>	<u>NOTES</u>
7-87	Moving Target Range  (LAW, SMAW & .50 Cal)	G-7	2d QTR FY 87	N/A	Base Maint  WR# 103-85	N/A	
8-87	Air Assault Landing  Zone/Drop Zone	LZ Falcon	4th Qtr FY 87	18-26 weeks  2d CEB and other  Mil. Engr units	N/A	\$200,000	3500 ft x 100
9-87	Company Level Live Fire  Assault Range	Around G-10  Expansion  Area	FY 87	TBD	Base Maint  (Elec SVC)  Contract	Unk	
10-87	Bridging Sites for  OT Testing of TLB	IA, IC area  & Duck Creek	2d Qtr FY 87	6 weeks  2d CEB and other  Mil Eng units	N/A	\$5,000	
11-87	Rappelling Tower/  Confidence Course	Camp Geiger/  Verona	FY 87	2d FSSG	N/A	\$15,000	

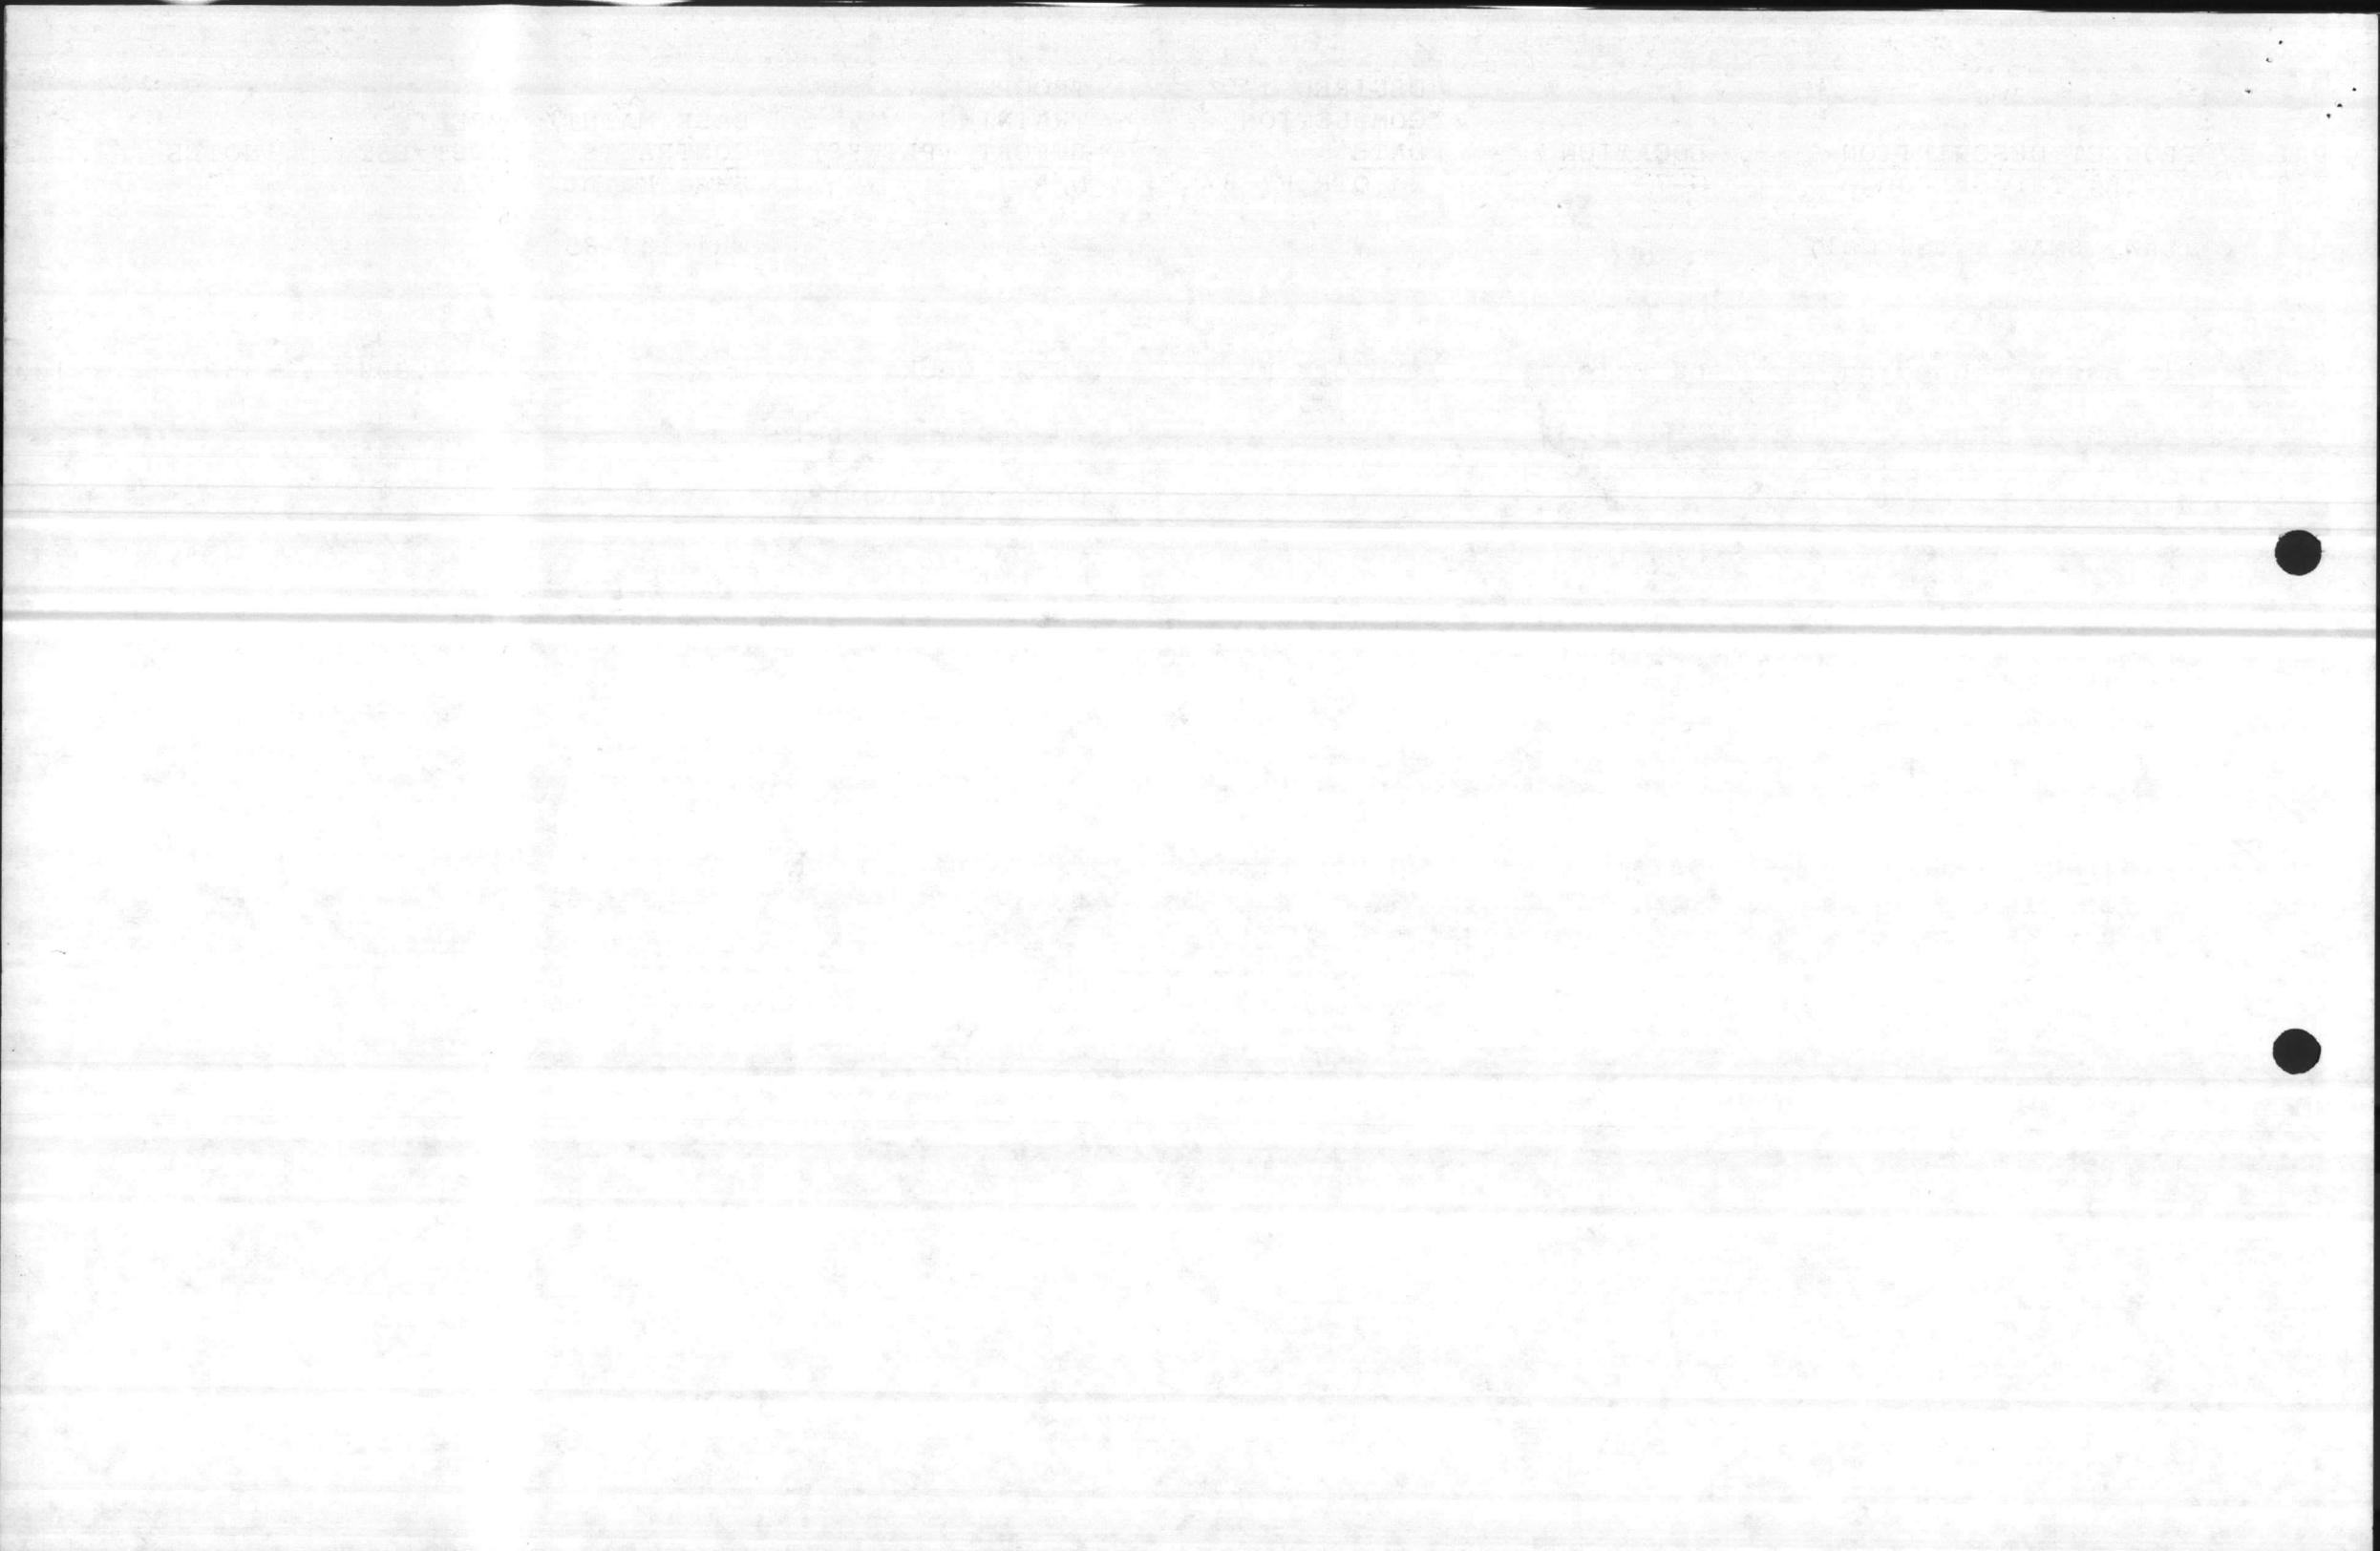

<u>PRI</u>	<u>PROJECT DESCRIPTION</u>	<u>LOCATION</u>	<u>DESIRED COMPLETION DATE</u>	<u>TROOP TRAINING EFFORT (PLTWKS)</u>	<u>BASE MAINT/ CONTRACTS</u>	<u>PRELIM COST EST</u>	<u>NOTES</u>
1-88	MOUT	F-Area	FY 88/89		Contract	\$ Million	
2-88	Rappelling Tower/ Confidence Course	K-Range Bivovac Area	FY 88	2d FSSG	N/A	\$15,000	
2-88	Rappelling Tower	Area 1/2	FY 88				
1-89	Extend Ranges for (improved) 81 MM Ammo (max tables)	TBD	FY 89	6 weeks	Contract	unk	
2-89	M2-50, M19 UPGUN for AAV Bn (simultaneous shoot)	Land Acquisition Area	FY 90	TBD	Contract (targets/ Elec SVC)	\$200,000	
3-89	Gun Positions VIC verona loop for MLRS & due to G-10 expansion MLRS in new land area fire south area <u>North-</u> ward	Land Acquisition Area	FY 89	Air Space questions			Tied to MLRS E ment

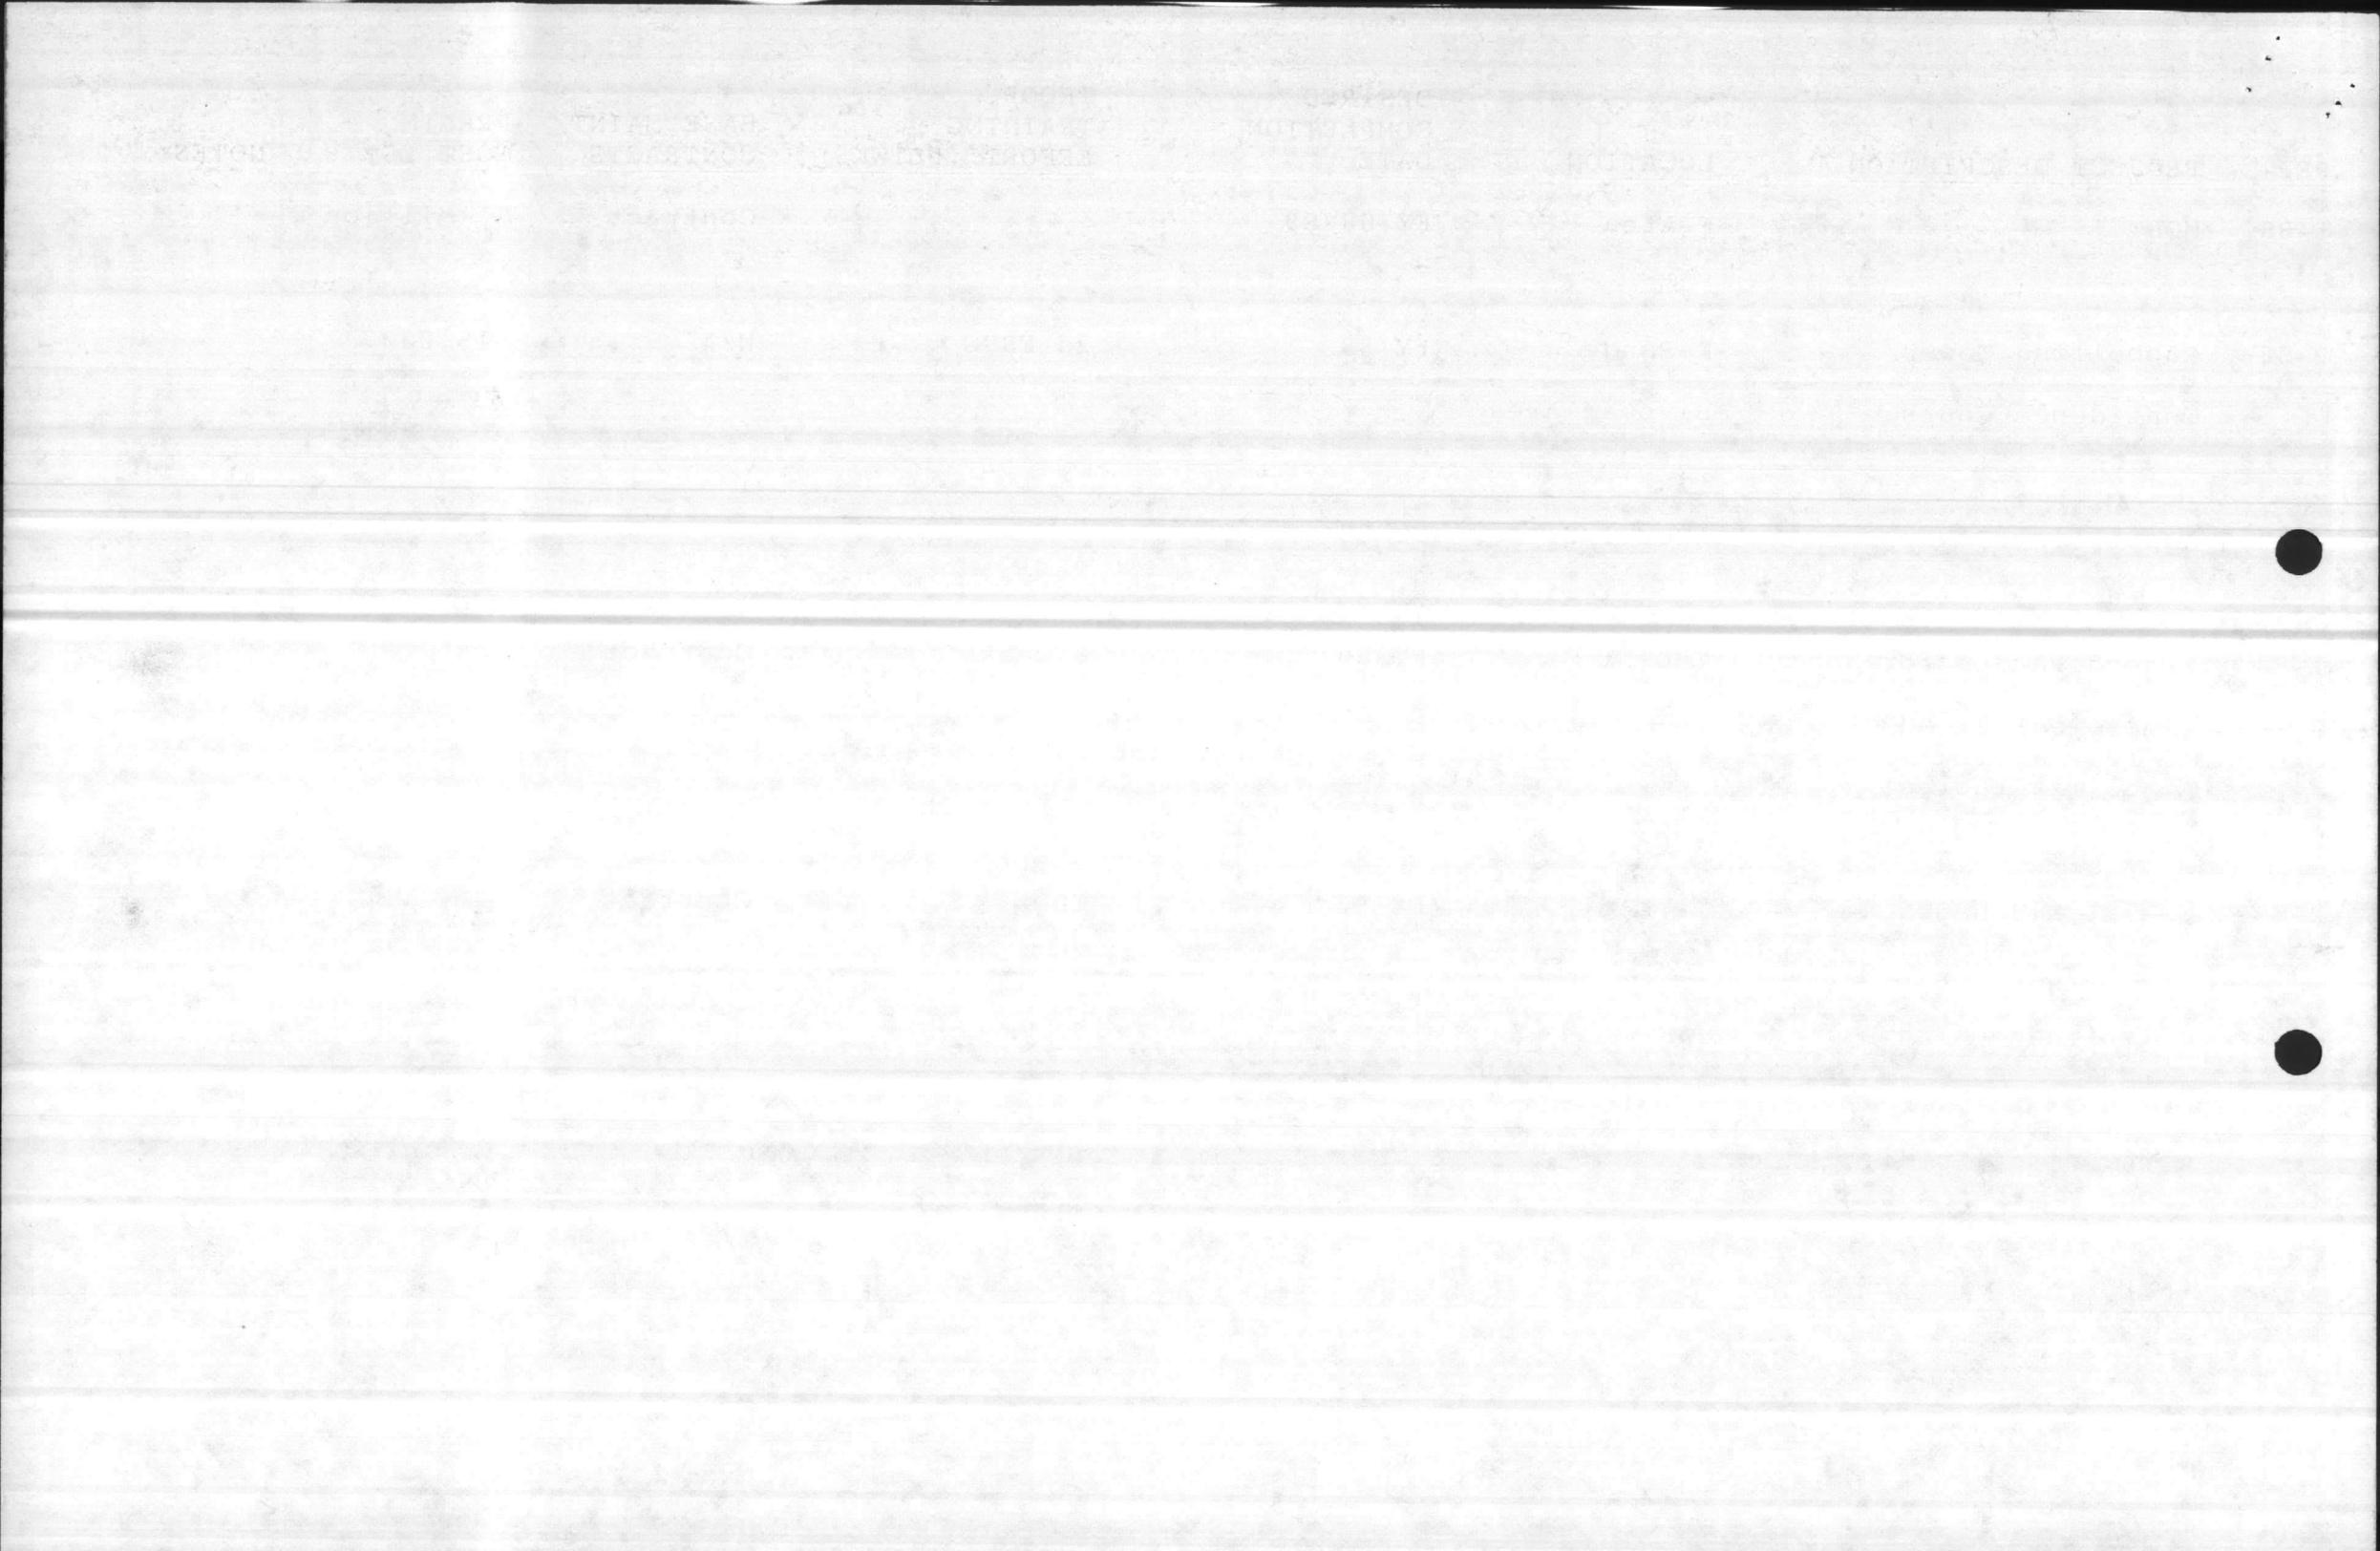

<u>PRI</u>	<u>PROJECT DESCRIPTION</u>	<u>LOCATION</u>	<u>DESIRED COMPLETION DATE</u>	<u>TROOP TRAINING EFFORT (PLTWKS)</u>	<u>BASE MAINT/ CONTRACTS</u>	<u>PRELIM COST EST</u>	<u>NOTES</u>
13-87	Airframes CH-46/53/C-130/141	Geiger/ Mainside	FY 87	TBD	Base Maint (Elev SVC)	\$25,000	
14-87	Tank Trails	Mainside LZ Jaybird LZ Dove & other locations	FY 87	15 weeks 2d CEB & other Mil Eng units	Base Maint WO-97-85 (Partial)	\$15-20,000	
15-87	Confidence Course	French Creek	Fy 87	2d FSSG	N/A	\$15,000	

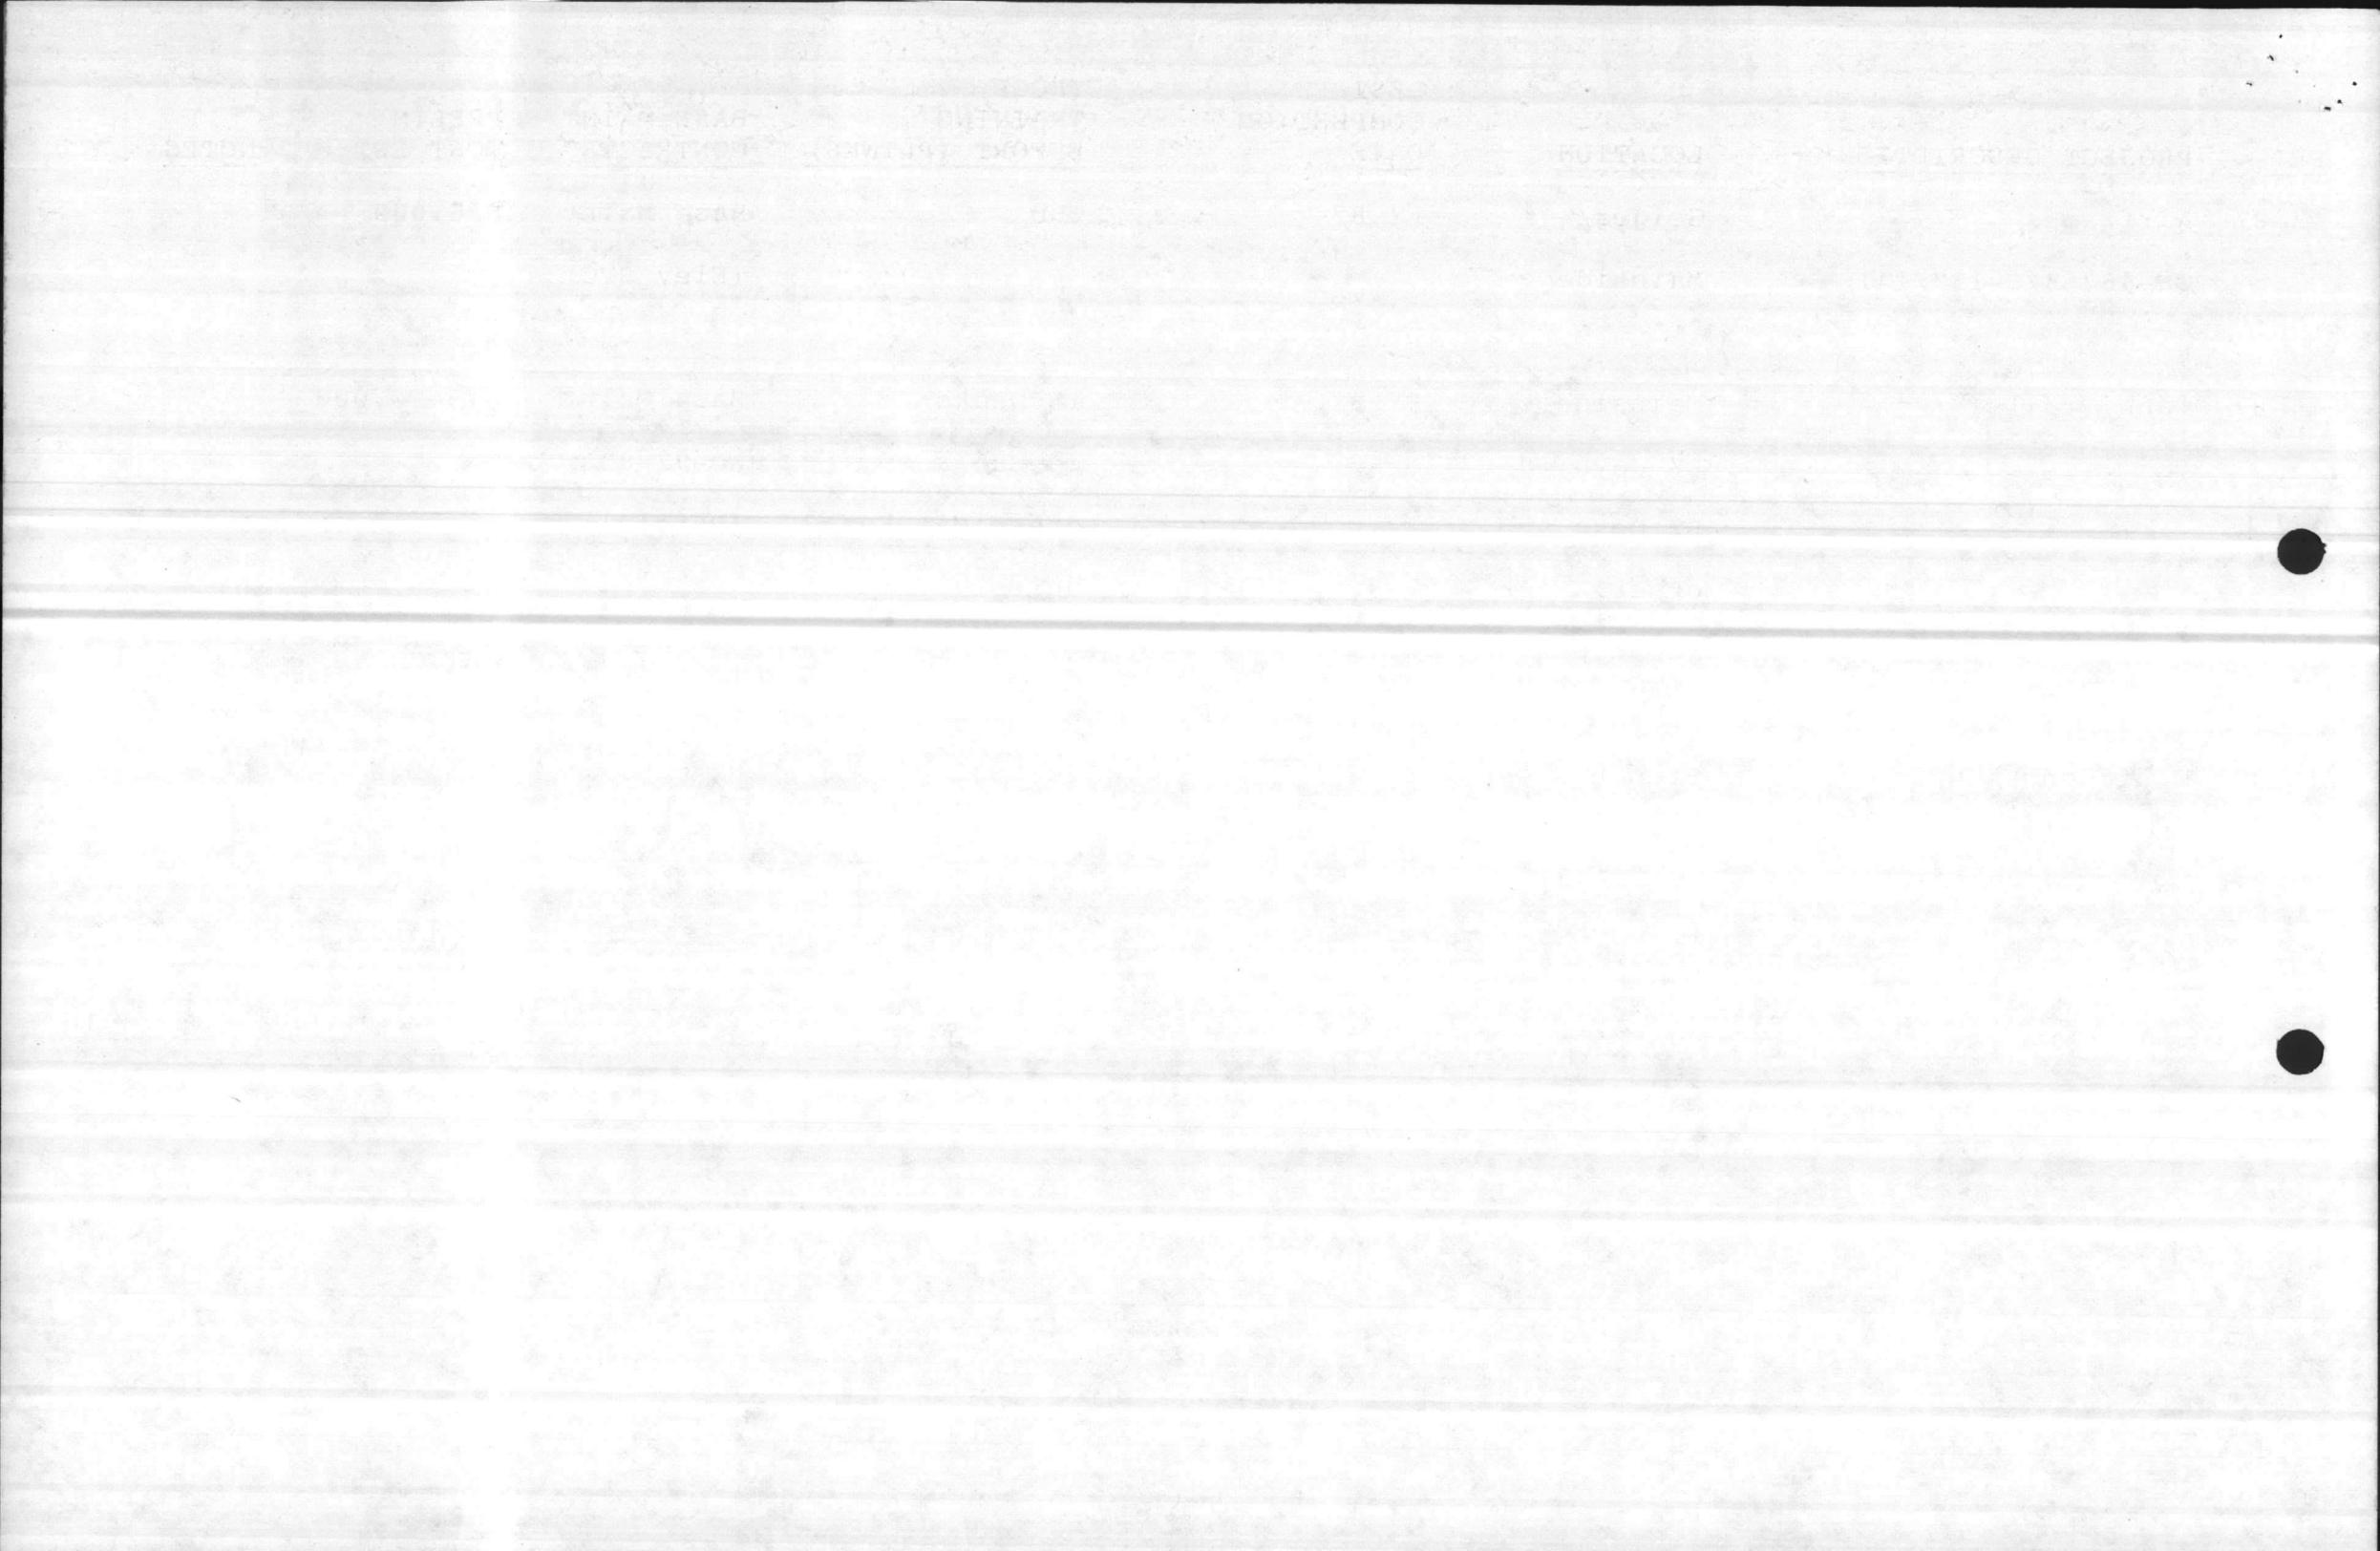

<u>PRI</u>	<u>PROJECT DESCRIPTION</u>	<u>LOCATION</u>	<u>DESIRED COMPLETION DATE</u>	<u>TROOP TRAINING EFFORT (PLTWKS)</u>	<u>BASE MAINT/ CONTRACTS</u>	<u>PRELIM COST EST</u>	<u>NOTES</u>
1-90	Range/maneuver area complex, e. g., for M1 Tank Gun (120 MM)	Land Acquisition Area	FY 90	TBD	Contract  (targets)	TBD	
2-90	Highway 17 crossing pads	proposed land acquisition area hwy 17	FY 90	N/A	contract		
3-90	LCU/LCAC Boathouse/Ramp Navy Boat Crew	Mile Hammock Bay Area	FY 90/92	N/A	Contract	MCON	
4-90	CQ/Indoor Ranges		FY 90	N/A	MCON	unk	

