

CONTRACTOR'S SUBMITTAL TRANSMITTAL
 LANTDIV NORFOLK 4-4355/3 (Rev. 11-80)

40/RVK
 102

Feli

FROM CONTRACTOR
 Trader Construction Company
 TO
 Lockwood Greene/Six Associates

CONTRACT NO. 81-C-1766
 TRANSMITTAL NO. 778 77C
 DATE July 23, 1984
 PROJECT TITLE AND LOCATION
 Public Works
 MCB
 Camp Lejeune, N. C.

CONTRACTOR USE ONLY

REVIEWER USE ONLY

*List only one specification division per form.
 List only one of the following categories on each transmittal form, and indicate which is being submitted

****ACTION CODES**
 A-Approved
 D-Disapproved
 AN-Approved as noted
 RA-Receipt acknowledged.
 C-Comments
 R-Resubmit

Contractor Approved

OICC Approval

Deviation/Substitution For OICC Approval

ITEM NO.	PROJ. SPEC. SECT. & PARA. and/or PROJ. DWG. NO.	ITEM IDENTIFICATION (Type, size, model no., Mfg. name, dwg. or brochure number)	NO. OF COPIES	ACTION CODES **	REVIEWER'S INITIALS CODE AND DATE
144	09250	Gypsum Wallboard			
	2.1.1	Gypsum tapered panels, cert..	7	A	<i>A/C.A.B. 30 July 84</i>
		5/8" Sheetrock Firecode panels, cert.	7	A	
	2.1.2	Sheetrock water-resistant panels, cert.	7	A	
		Drawings for GWB in detail	7	AN	

CONTRACTOR'S COMMENTS

Fiber-glass reinforced concrete board, cert. and catalog data en route

COPY OF TRANSMITTAL AND SUBMITTALS TO ROICC

ROICC, Camp Lejeune, N. C.
 DATE RECEIVED BY REVIEWER 7/26/84

CONTRACTOR REPRESENTATIVE (Signature)

Ms Dale Stallings

FROM (Reviewer)

Six Associates, Inc.

TO

Trader Construction Co.

- Submittals are returned with action indicated. Approval of an item does not include approval of any deviation from the contract requirements unless the contractor calls attention to and supports the deviation.
- Submittals are forwarded to LANTDIV with A-E recommendations indicated in REVIEWER USE ONLY Section and in comments below on ONE COPY of the transmittal form.

REVIEWER'S COMMENTS

This submittal is confusing. Rib-lath should be in another section.

*Copy to Feli
 8-8-84
 me*


COPIES TO:
 ROICC (2) ✓
 LANTDIV (1)
 A-E (1)

DATE

July 31, 1984

SIGNATURE

A.B. John

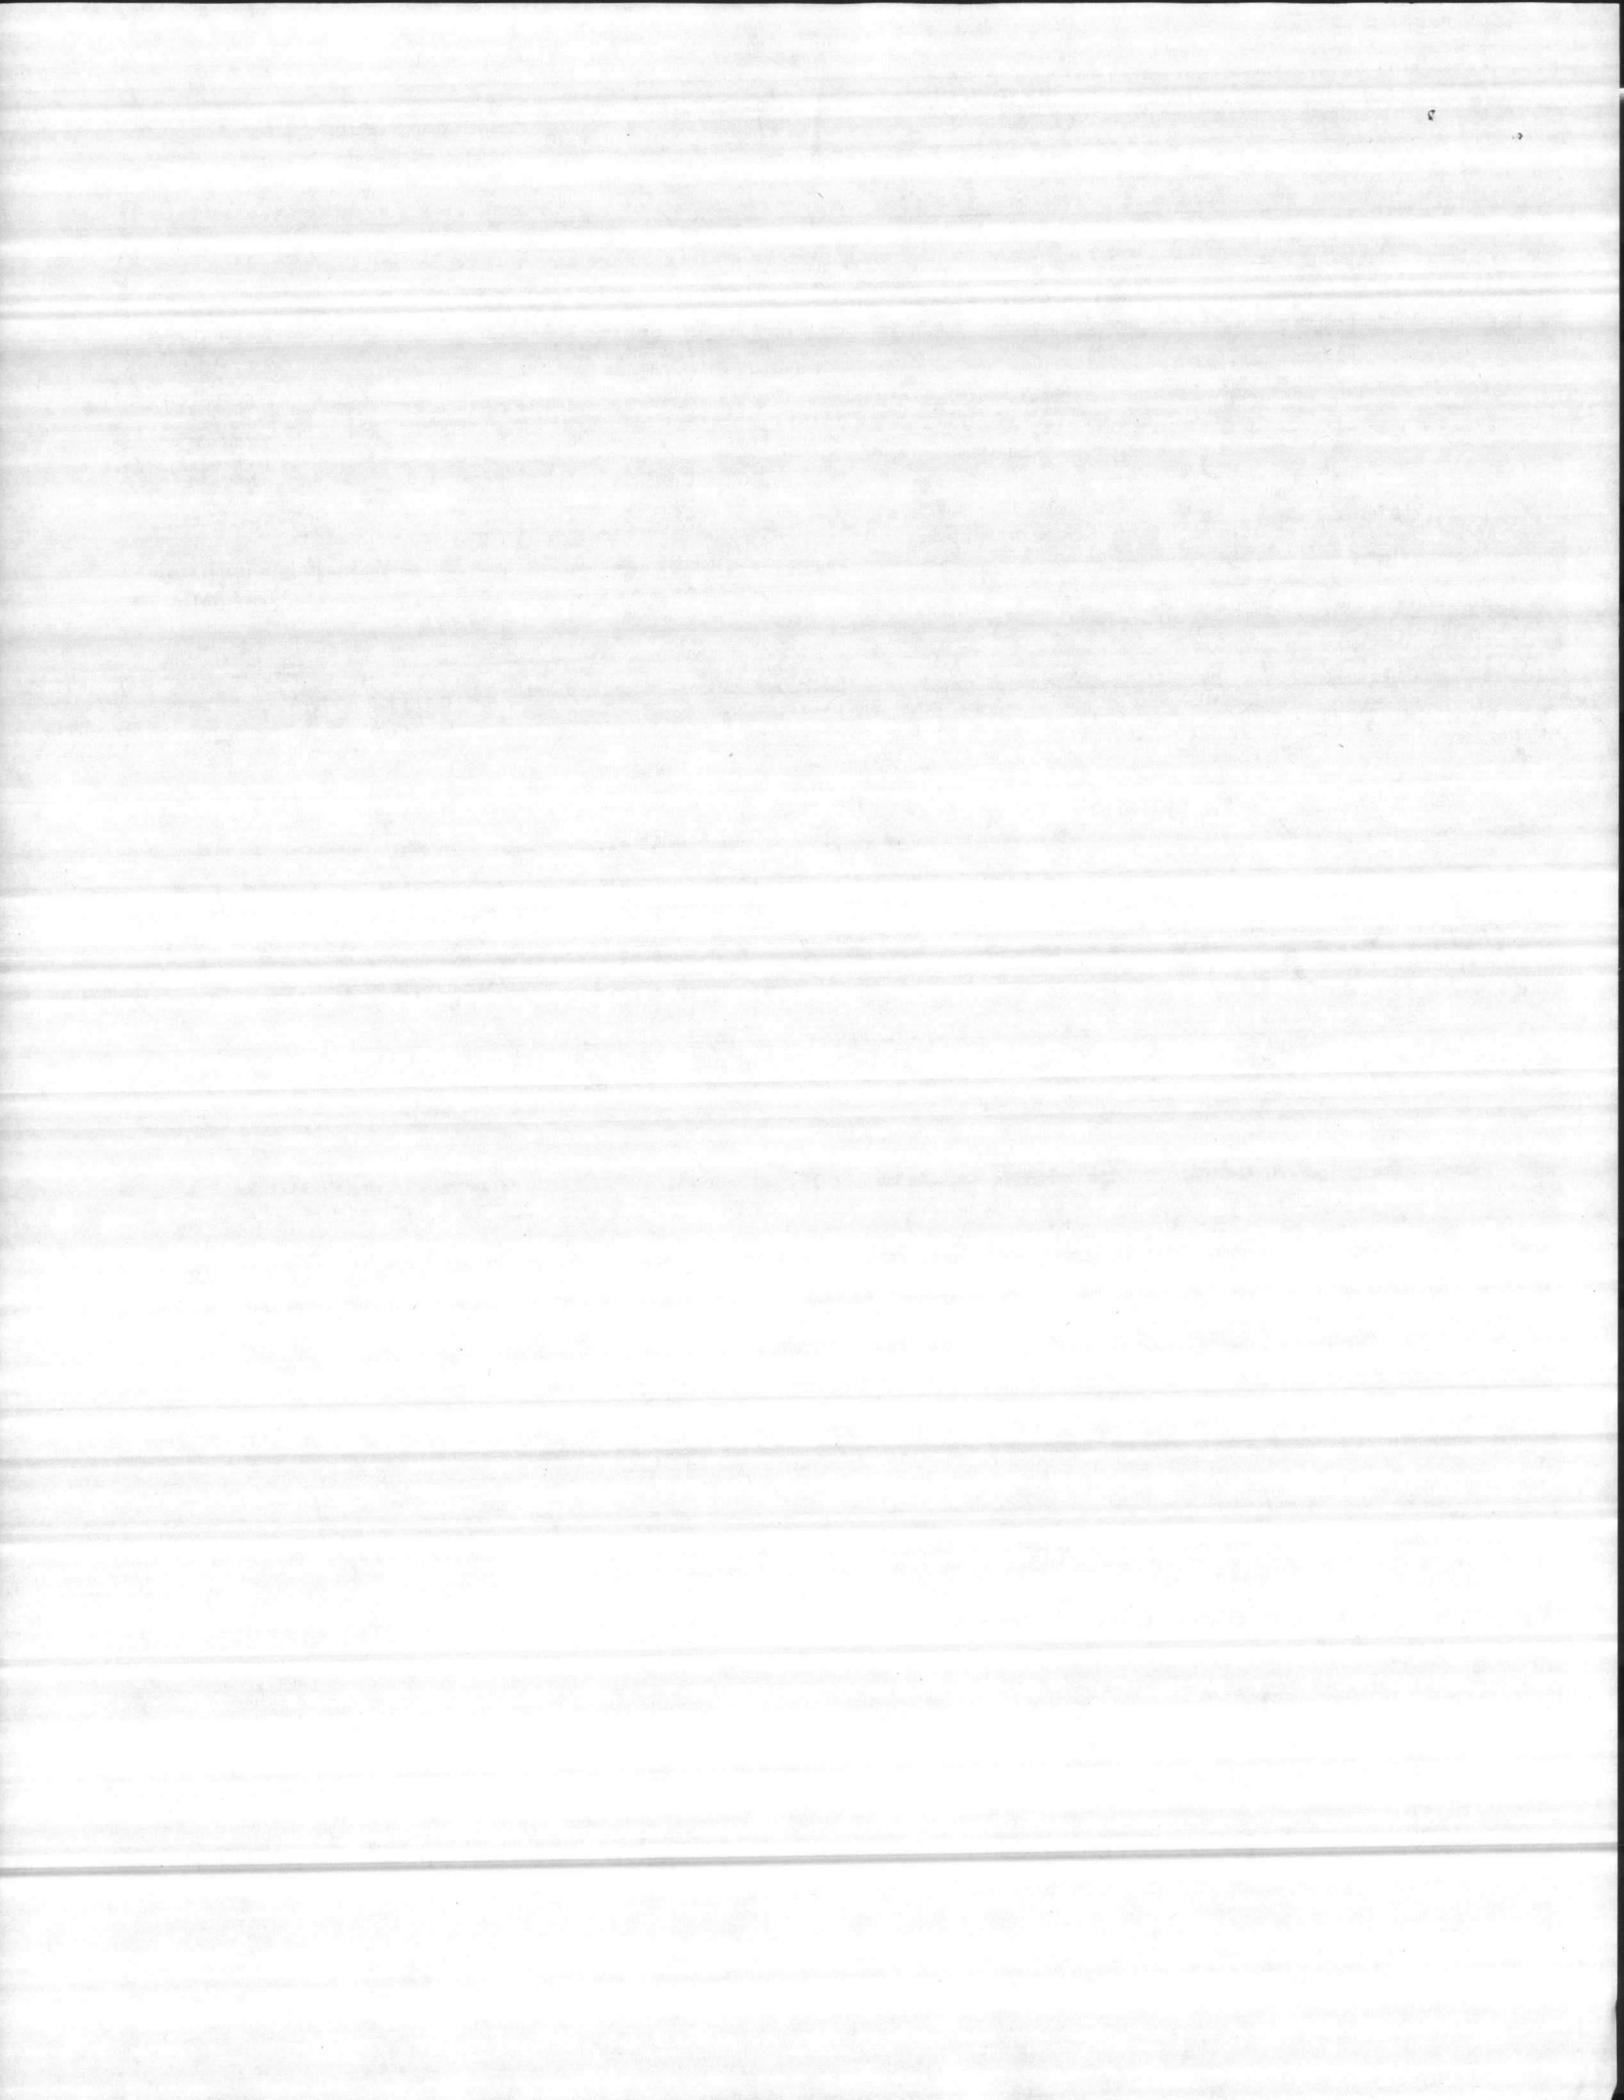

UNITED STATES GYPSUM COMPANY //

1500 Forest Ave., / Richmond, Virginia 23288

ATLANTIC DIVISION
NAVAL FACILITIES ENGINEERING COMMAND
NORFOLK, VIRGINIA 23511

June 12 1984

APPROVED _____
APPROVED AS NOTED _____
DISAPPROVED _____

SUBJECT TO THE REQUIREMENTS OF
CONTRACT NO. 162470-81-C-1766

APPROVAL OF A SUBMITTAL DOES NOT INCLUDE
APPROVAL OF ANY DEVIATION FROM THE CONTRACT
REQUIREMENTS UNLESS THE CONTRACTOR
CALLS ATTENTION TO AND SUPPORTS THE DEVIATION...
THE CONTRACTOR SHALL BE RESPONSIBLE FOR PROVIDING
PROPER PHYSICAL DIMENSION & WEIGHTS, COORDINATION OF TRADES, ETC., AS
REQUIRED.

REVIEWER [Signature] 30 [Signature] 1984
DATE

FOR OFFICER IN CHARGE OF CONSTRUCTION

Interior Distributors Inc
P O Box 14126
1105 New Hope Rd
Raleigh NC 27620

CERTIFICATION OF MATERIALS FOR


Public Works
Camp LeJeune NC
Contract 81-C-1766

We, the undersigned, certify that the following materials supplied by us for use on the Public Works, Camp LeJeune NC job comply with requirements and tests of the federal specifications for each product as indicated below and are guaranteed by us.

<u>PRODUCTS</u>	<u>FED SPECIFICATIONS</u>	<u>ASTM DESIGNATIONS</u>
Sheetrock brand tapered edge Gypsum Panels	SS-L-30D type III grade R class 1	C36
5/8" Sheetrock brand Firecode Gypsum Panels	SS-L-30D type III grade X class 1	C36
Sheetrock brand W/R water-resistant Gypsum Panels	SS-L-30D type VII grade W or X class 2	C630
USG & Durabond joint compounds	SS-J-570B type I	C475

"It is hereby certified that the (equipment) (material, shown and marked in this submittal is that proposed to be incorporated into Contract Number 162470-81-C-1766 is in compliance with the Contract drawings and specifications, can be installed in the allocated spaces, and is in full Government approval.

Certified by D. Stallings
Date 7-23-84

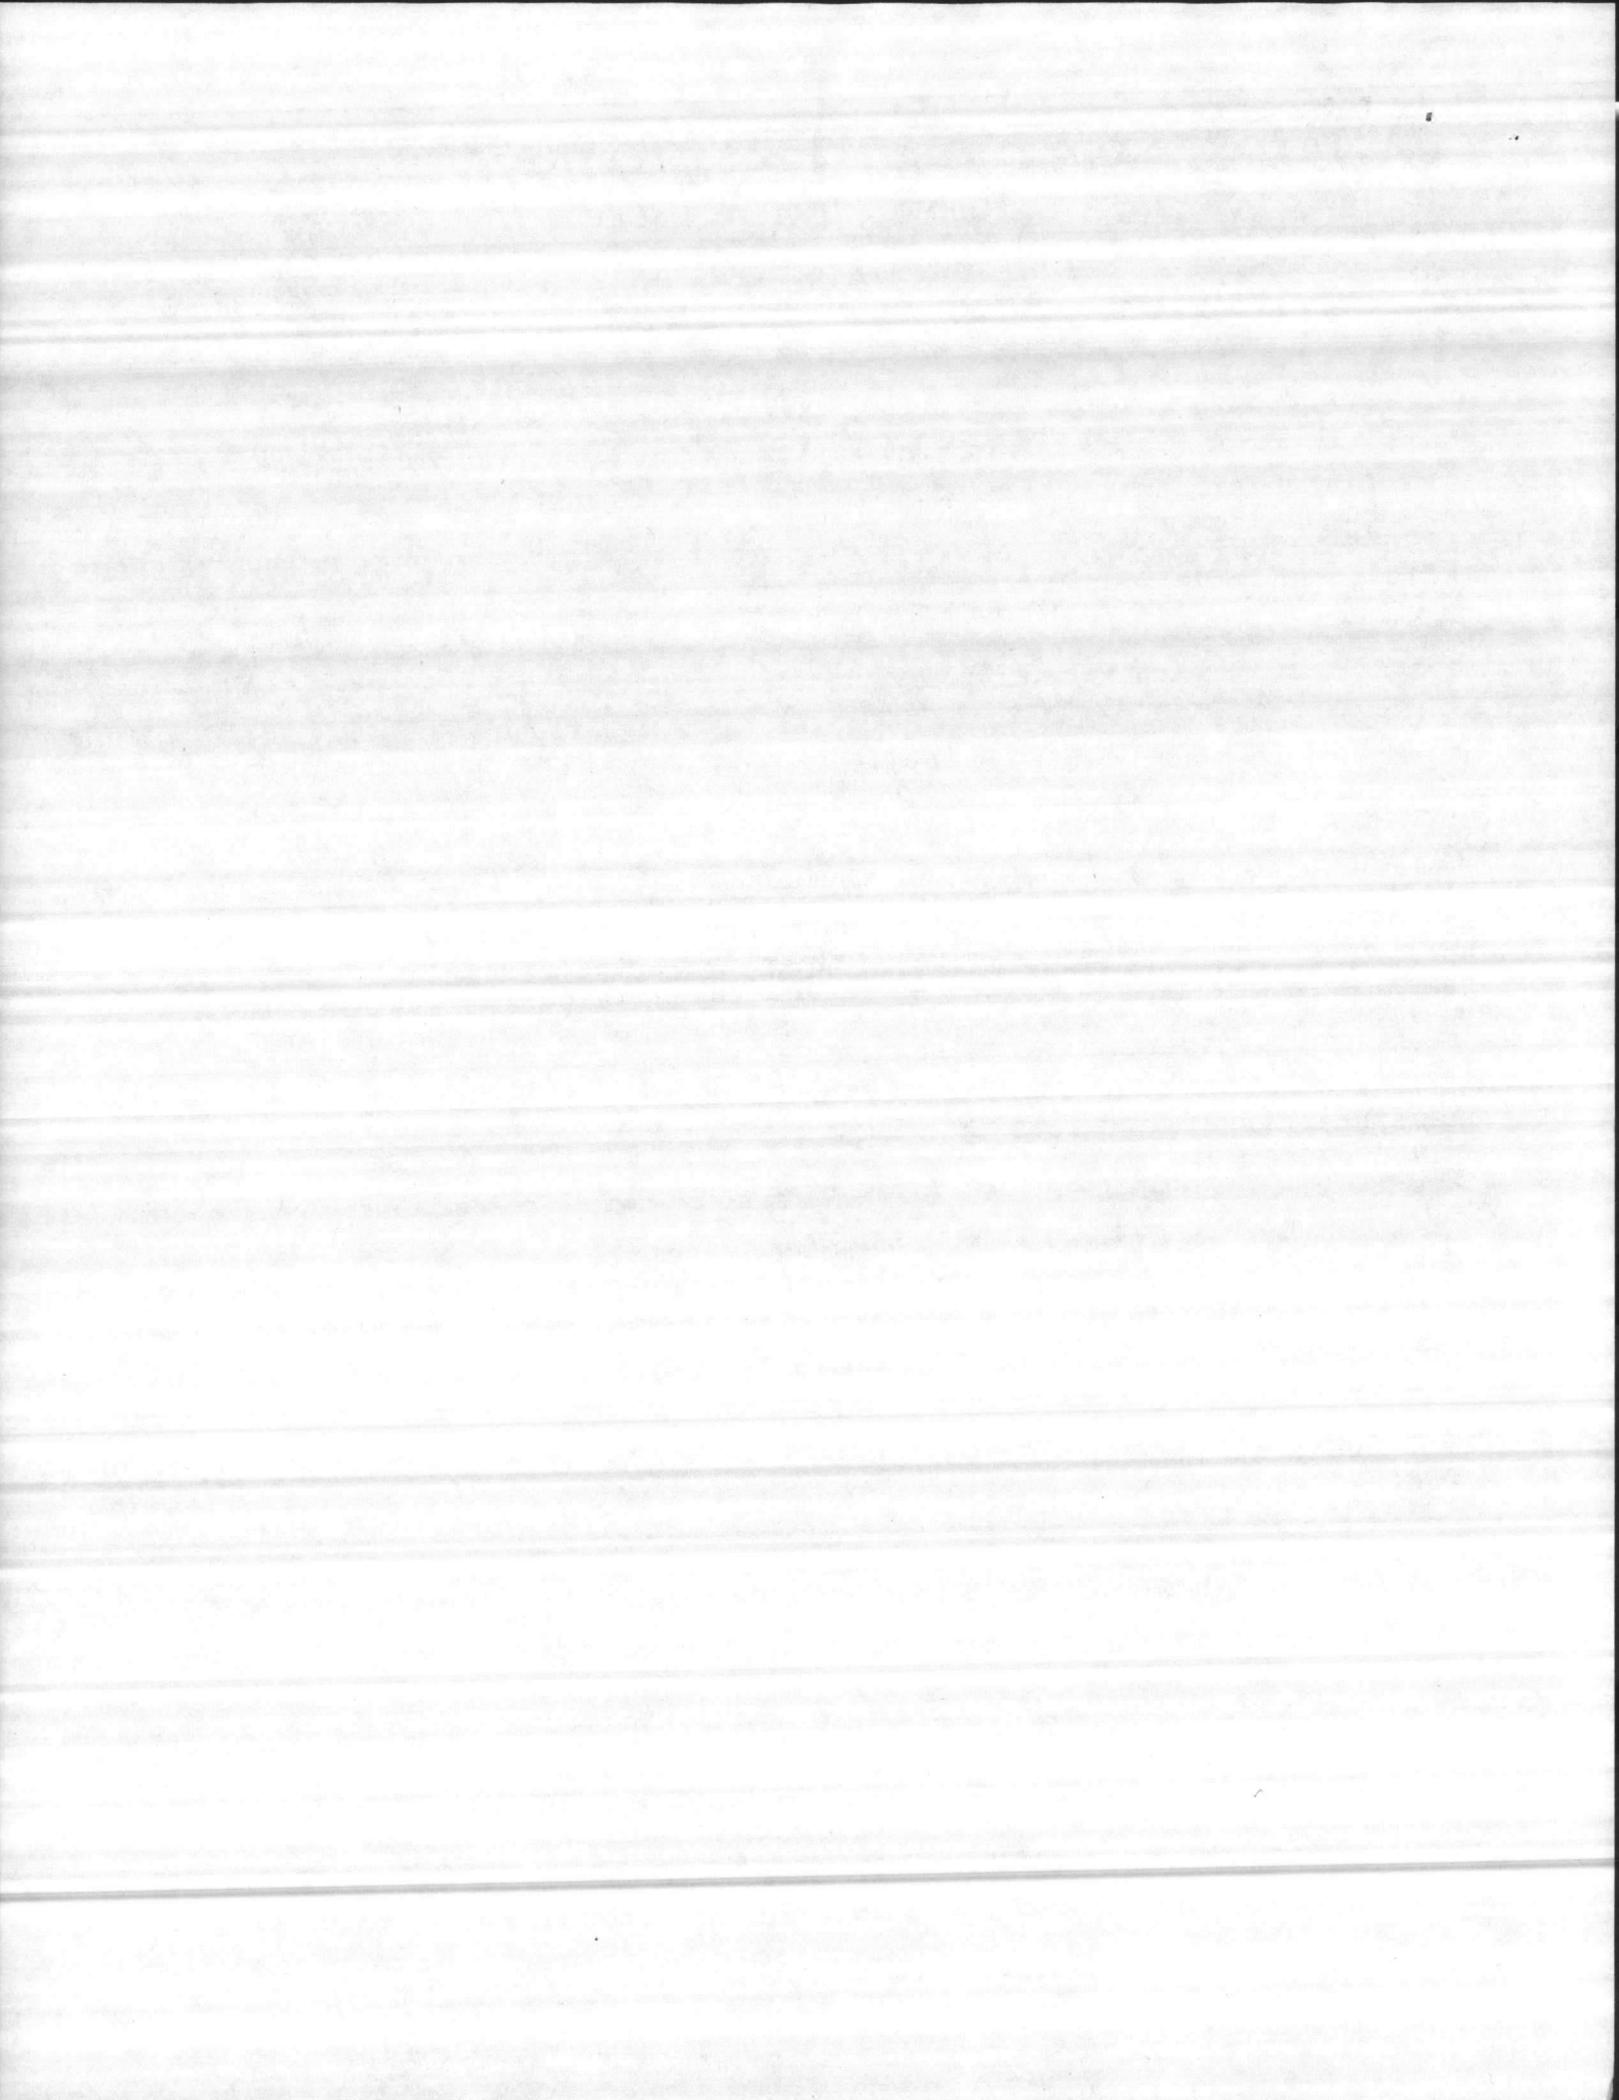

PRODUCTS

FED SPECIFICATIONS

ASTM DESIGNATION

Bases, metal:(for)plaster,lath
and stucco constr(WC)
3.4# galv diamond mesh
lath, 2.5# and 3.4# ptd.,1/8"
4-mesh z-rib lath 2.75# and
3.4#; 3/8" rib lath 3.4#;
stucco mesh 1.8#

QQ-L-101C
class 3(flat dia mesh)
class 3(self furring
dia mesh)
class 4(1/8" flat rib)
class 1(3/8" rib)
class 6(stucco mesh)

09110
L? A/E

Very truly yours

UNITED STATES GYPSUM COMPANY

S.W. Carey

S W Carey
Field Sales Manager

Subscribed and sworn to
before me this 19th
day of June 1984.


Quetta S Payne
Notary

My Commission Expires 4/7/85

"It is hereby certified that the (equipment)
(material) shown and marked in this submittal
is that proposed to be incorporated into
Contract Number 1162470-81-C-176 in
compliance with the Contract drawings and
specifications, can be installed in the allocated
space, and is submitted Government
approval.

Certified by D. Stallings

Date 7-23-84

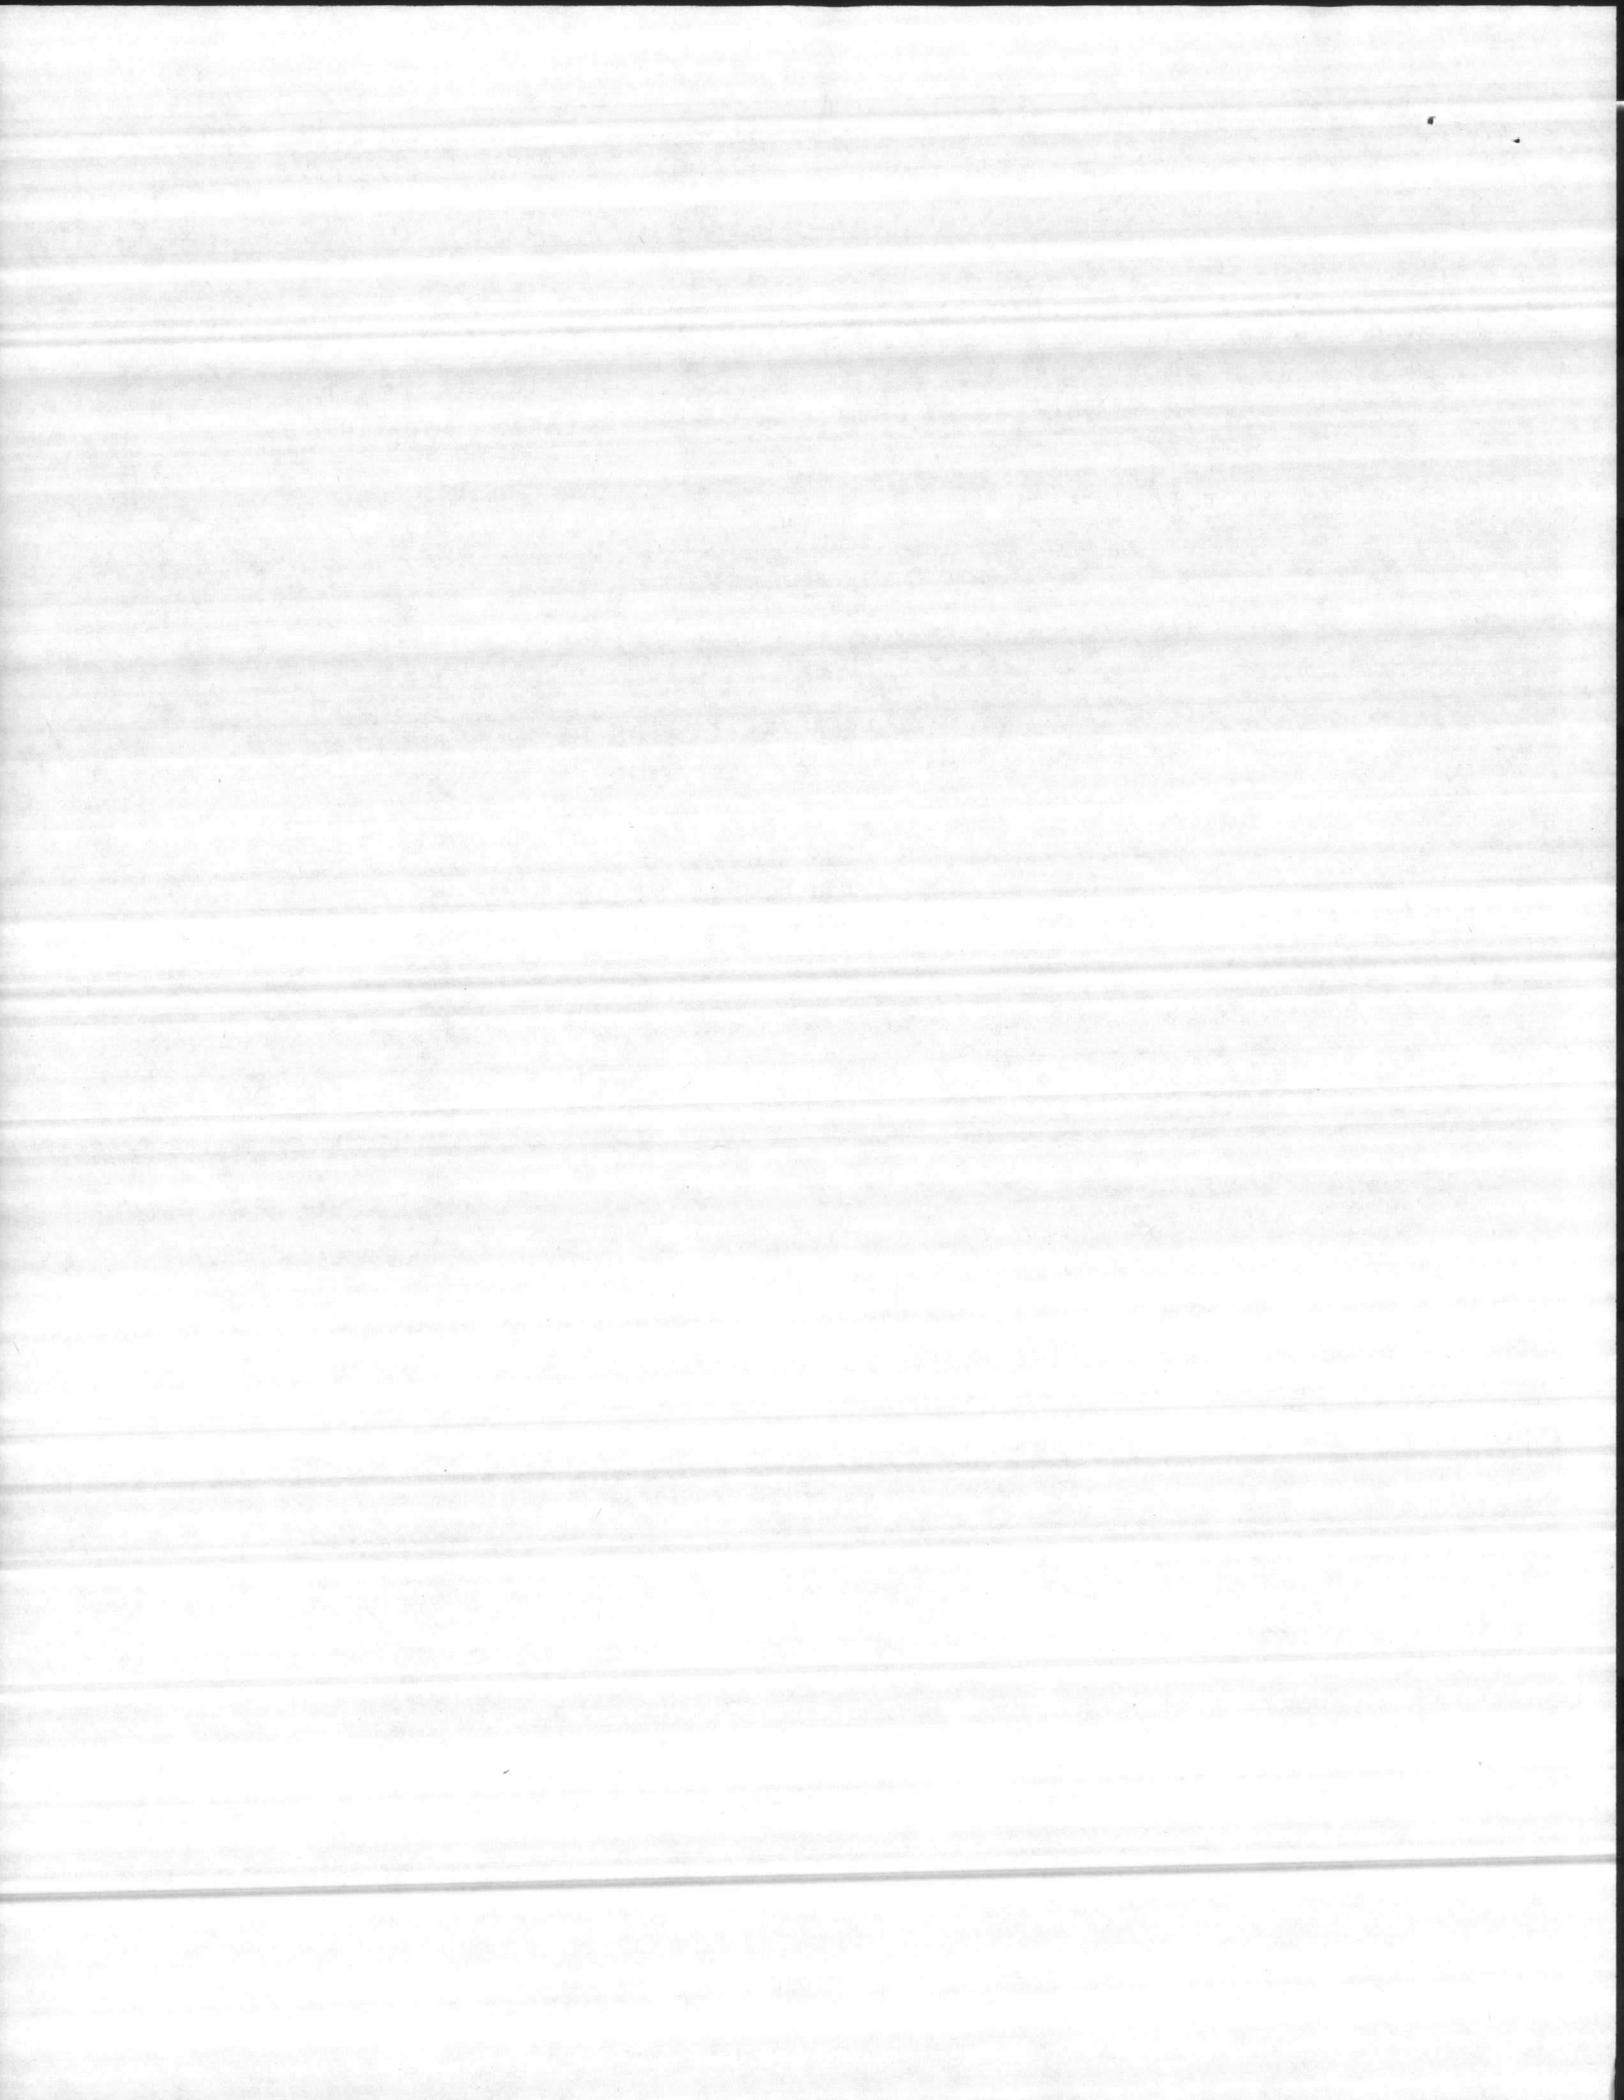

Camp Lejeune, N. C.

Shop Drawings By C. H. Bryant Pla. Co.

4" x 16 Ga Studs at doors easide

4" x 20 Ga Track at Door Header

ea 4' of Elev
Wall Stiffener
1 ea 1 1/2 Cold Roll Channel

Regular Partition Framing

use 1" S-12 screws at Decking Ect.

Top 4" x 20 Ga Track

S-12 Pan Head Screw

ea Side Bottom + Top

Sound Attenuation blankets

Chase Wall Framing

Galv
R+ins
Wall
Spacers
4" o.c.

1/2"

1/2" o.c.

5/8 Galv B

Type S-12 x 1" screws

Metal Trim at Block

1/4" Sealant at Floor

1" Power Fasteners 24" Apart at Bottom Track

1/4" Galv B Corner Bead ea side

1" S-12 Screws at Door Anchors

4" x 16 Ga Studs at Doors

SEE SH. A-3

Corner Detail

4" x 20 Ga Stud + Track

5/8 Galv B

Partition end Detail

Metal Door Jam Detail

Partition Intersection

Reinforce Tape + Compound At all intersections + Joints

The Above Gives in Detail Framing, Fasteners, Hanging, Sound Blankets + Trim

